




Transition Implementation Status Reporting

17 Jun 2016

1. Overall Timeline
2. Status Update
3. Appendix: Projects Plans

Overall Timeline


Implementation Planning Timeline – Proposals Delivered in March 2016

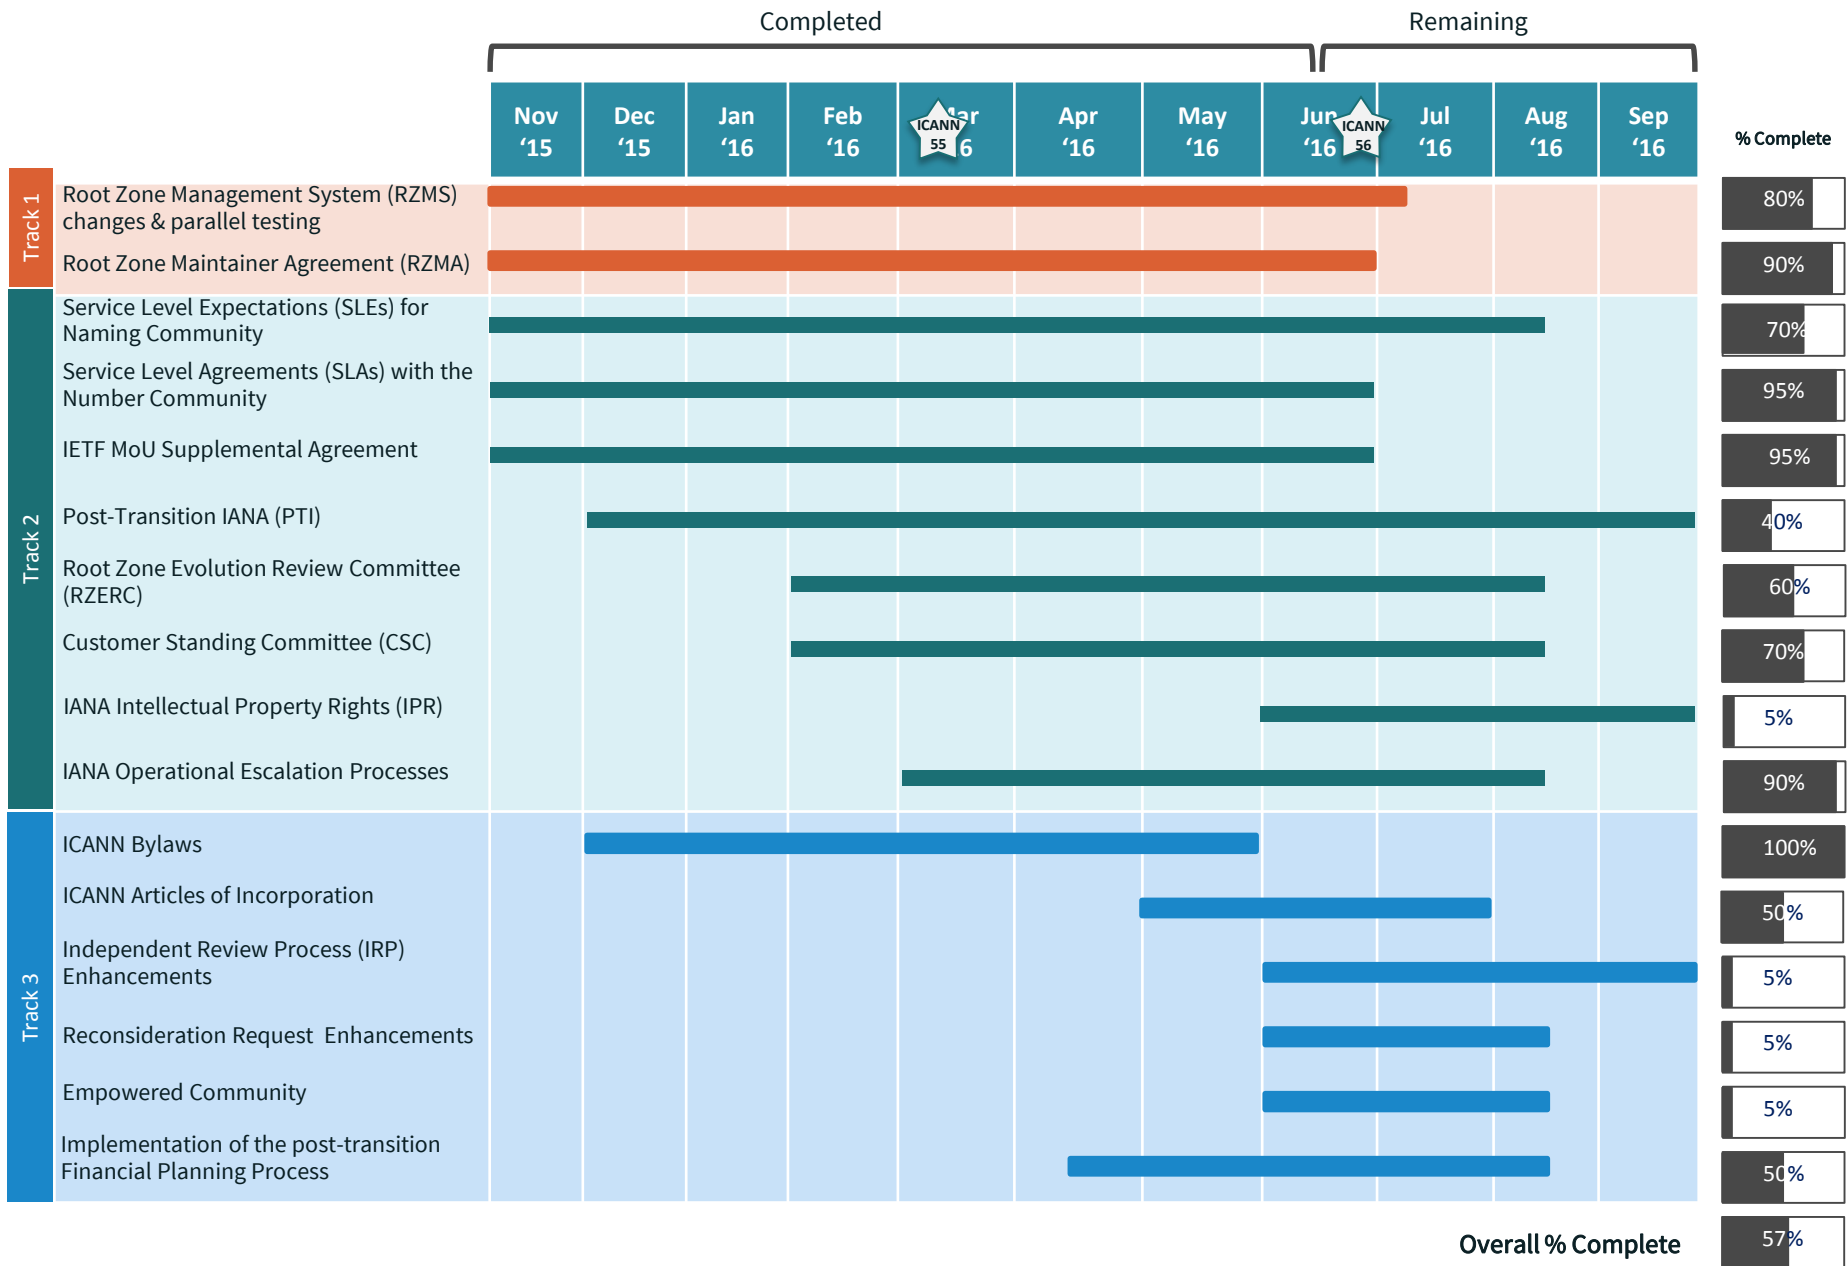

Status Update

Project	Description	Plan Completion Date	Status	% Complete
RZMS changes to remove RZA role and support parallel testing	Remove NTIA's authorization process from RZMS (code changes for ICANN and Verisign, and parallel testing).	09/30/16 08/15/16 07/06/16		80%
Names SLEs (SLEs for Naming Community)	RZMS code changes to accommodate new SLEs, inclusion of performance targets in ICANN-PTI contract, dashboard reporting of SLAs.	09/30/16 08/15/16		70%
RZMA (Agreement with Root Zone Maintainer)	Completion of draft RZMA.	01/31/16 / 02/29/16 04/15/16 / 04/30/16 05/15/16 / 05/31/16/ 06/30/16		90%

Key Dates:

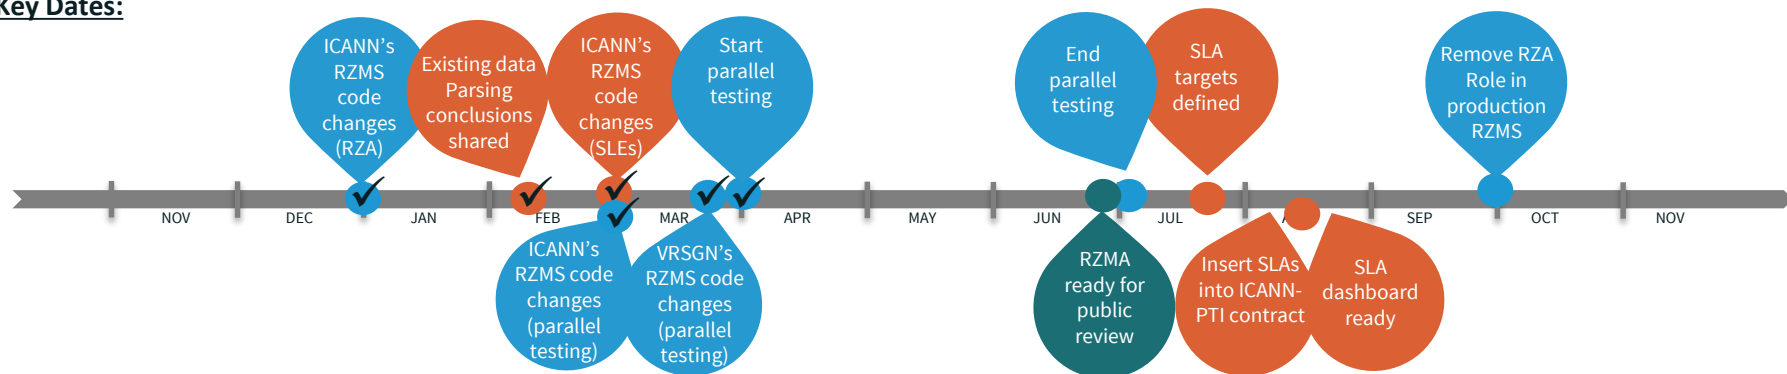

Project Updates:

- ✓ Completed 70 days of 90-day Parallel Testing period with no issues.
- ✓ SLE data collected since beginning of March is being aggregated and reviewed to propose performance targets.
- ✓ Continuing to work on the reporting dashboard.

Upcoming Activities:

- Continue to monitor parallel operations.
- Continue to fine-tune dashboard.
- Finalize proposed performance targets.
- Finalize draft RZMA.





Open Items:

(This section is currently empty)

RIRs SLAs & IETF MoU Supplemental Agreement


Status As Of Date:

06/15/16

Project	Description	Plan Completion Date*	Status	% Complete
RIRs SLAs (Service Level Agreement with the Number Community)	Completion of draft agreement, including SLAs with RIRs, and operationalization of SLAs.	06/30/16		 95%
IETF MoU Supplemental Agreement	Completion of draft ICANN-IETF MoU Supplemental Agreement.	06/30/16		 95%

* Completion Date dependent on USG's approval of proposals

Key Dates:

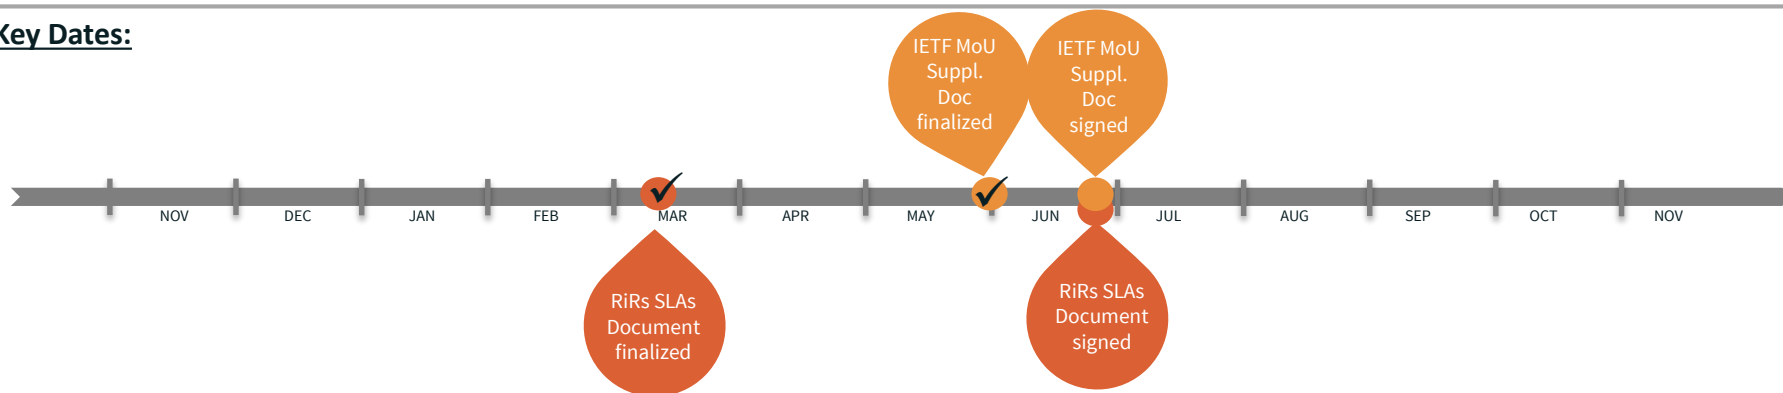

Project Updates:



Upcoming activities:



- Signing of the RIR SLA document
- Signing of the IETF MoU document

Open Items:



DRAFT for Discussion


-  On-track
-  Behind schedule, but recovery still possible

-  Not started
-  Target will be missed

* All dates are estimates

Project	Description	Plan Completion Date	Status	% Complete
PTI (Post-Transition IANA)	Formation of PTI entity: legal formation (incorporation of affiliate, filing for 501c3, drafting of contract, etc.) and operationalization of PTI entity (board nominations, budget, etc.).	09/30/16 08/15/16 09/30/16		40%

Key Dates:

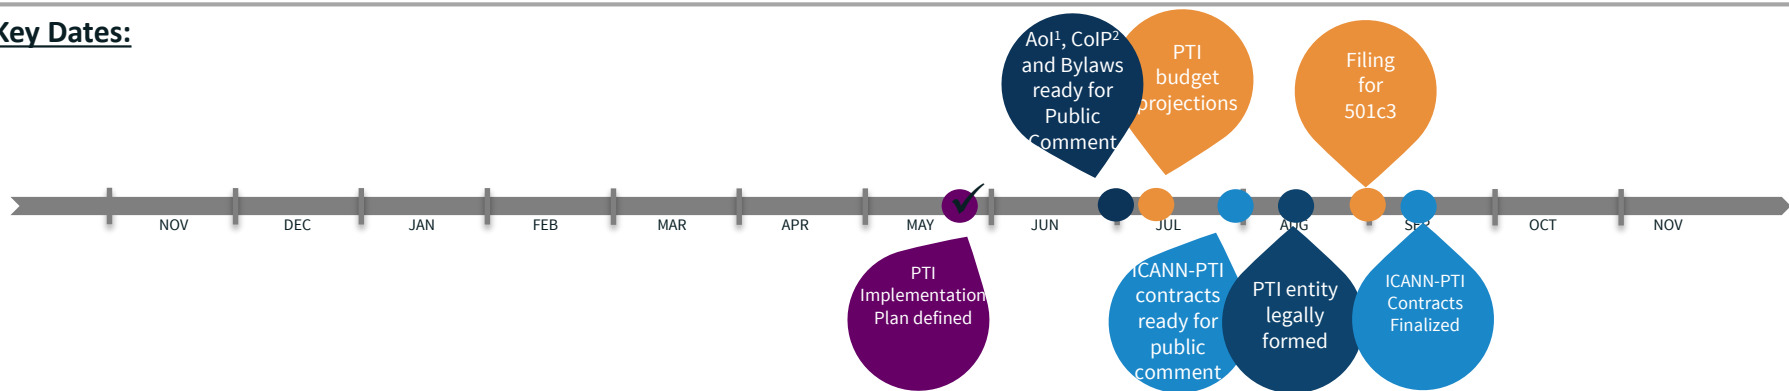

¹ Aol: Articles of Incorporation / ²CoIP: Conflicts of Interest Policy

Project Updates:

- ✓ Shared PTI staffing rationale with the community.
- ✓ Drafting of the ICANN-PTI contracts.
- ✓ Drafting of PTI conflict of interest policy, code of conduct and expected standard of behavior.

Upcoming activities:

- Finalize PTI Bylaws and articles of incorporation with the community.
- Share draft of Naming function contract with the community.
- Share PTI conflict of interest policy, code of conduct and expected standard of behavior with the community.

Open Items:



On-track



Not started



Behind schedule, but recovery still possible



Target will be missed

PTI Structure activities

Incorporation activities

501 c3 filing activities

ICANN-PTI contracts activities


IPR, RZERC, CSC & Escalation Processes

Status As Of Date:

06/15/16

Project	Description	Plan Completion Date	Status	% Complete
IANA IPR	Transfer of IANA IPR to a neutral trust.	9/30/16		<div style="width: 5%;"><div style="width: 5%;"></div></div> 5%
RZERC (<i>Root Zone Evolution Review Committee</i>)	Formation of committee to advise ICANN Board on RZMS architectural and operational changes.	09/30/16 08/15/16		<div style="width: 60%;"><div style="width: 60%;"></div></div> 60%
CSC (<i>Customer Service Standing Committee</i>)	Formation of committee to monitor PTI performance.	09/30/16 08/15/16		<div style="width: 70%;"><div style="width: 70%;"></div></div> 70%
Escalation Processes	Updating of existing IANA operational complaint and escalation processes.	09/30/16 08/15/16		<div style="width: 90%;"><div style="width: 90%;"></div></div> 90%

Key Dates:

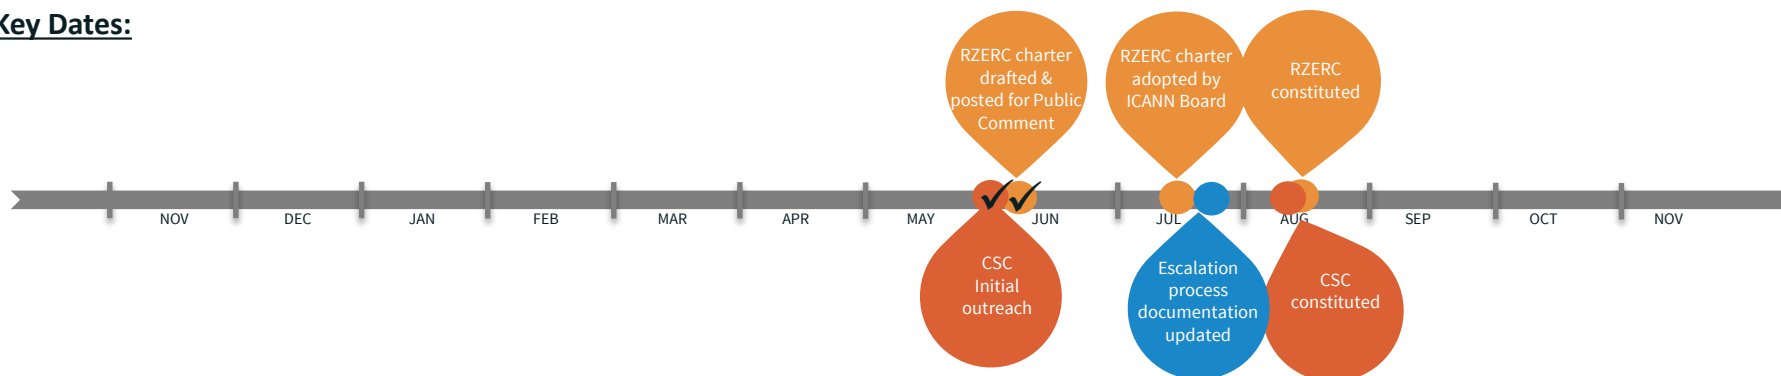

Project Updates:

- ✓ RZERC charter posted for public comments.
- ✓ CSC request for appointments sent to SO/ACs.
- ✓ Escalation processes documentation being updated.

Upcoming Activities:

- Monitor public comments on RZERC charter.
- Appointing organizations appoint CSC candidates.
- Finalize escalation processes documentation.

Open Items:

- Waiting on implementation requirements for IANA IPR.



DRAFT for Discussion

- On-track
- Behind schedule, but recovery still possible
- Not started
- Target will be missed

* All dates are estimates


Enhancing ICANN's Accountability

Status As Of Date:

06/15/16

Project	Description	Plan Completion Date	Status	% Complete
ICANN's Bylaws	Updating of ICANN Bylaws.	06/09/16 05/27/16		100%
ICANN's Articles of Incorporation (Aol)	Updating of ICANN Articles of Incorporation	07/31/16		50%
IRP Enhancements	Implement enhancements to Independent Review Process.	09/30/16 – 08/15/16 09/30/16		5%
RR Enhancements	Implement enhancements to ICANN's reconsideration request process.	09/30/16 08/15/16		5%
Empowered Community Enhancements	Implement processes and mechanisms in support of the empowered community.	09/30/16 08/15/16		5%
Financial Planning Process Updates	ICANN caretaker budget, PTI caretaker budget and PTI budget.	08/15/16		50%

Key Dates:



Project Updates:

- ✓ ICANN Articles of Incorporation posted for 40-day Public Comment period.
- ✓ Started initial assessment of items needed to support the Empowered Community.

Upcoming Activities:

- Monitor public comments on ICANN Aol.
- Finalize financial planning process.

Open Items:



DRAFT for Discussion

- On-track
- Behind schedule, but recovery still possible
- Not started
- Target will be missed

* All dates are estimates | 10




Appendix High-Level Project Plans

RZMS & SLEs for Naming Community

% Complete:  70%


Status: On-track

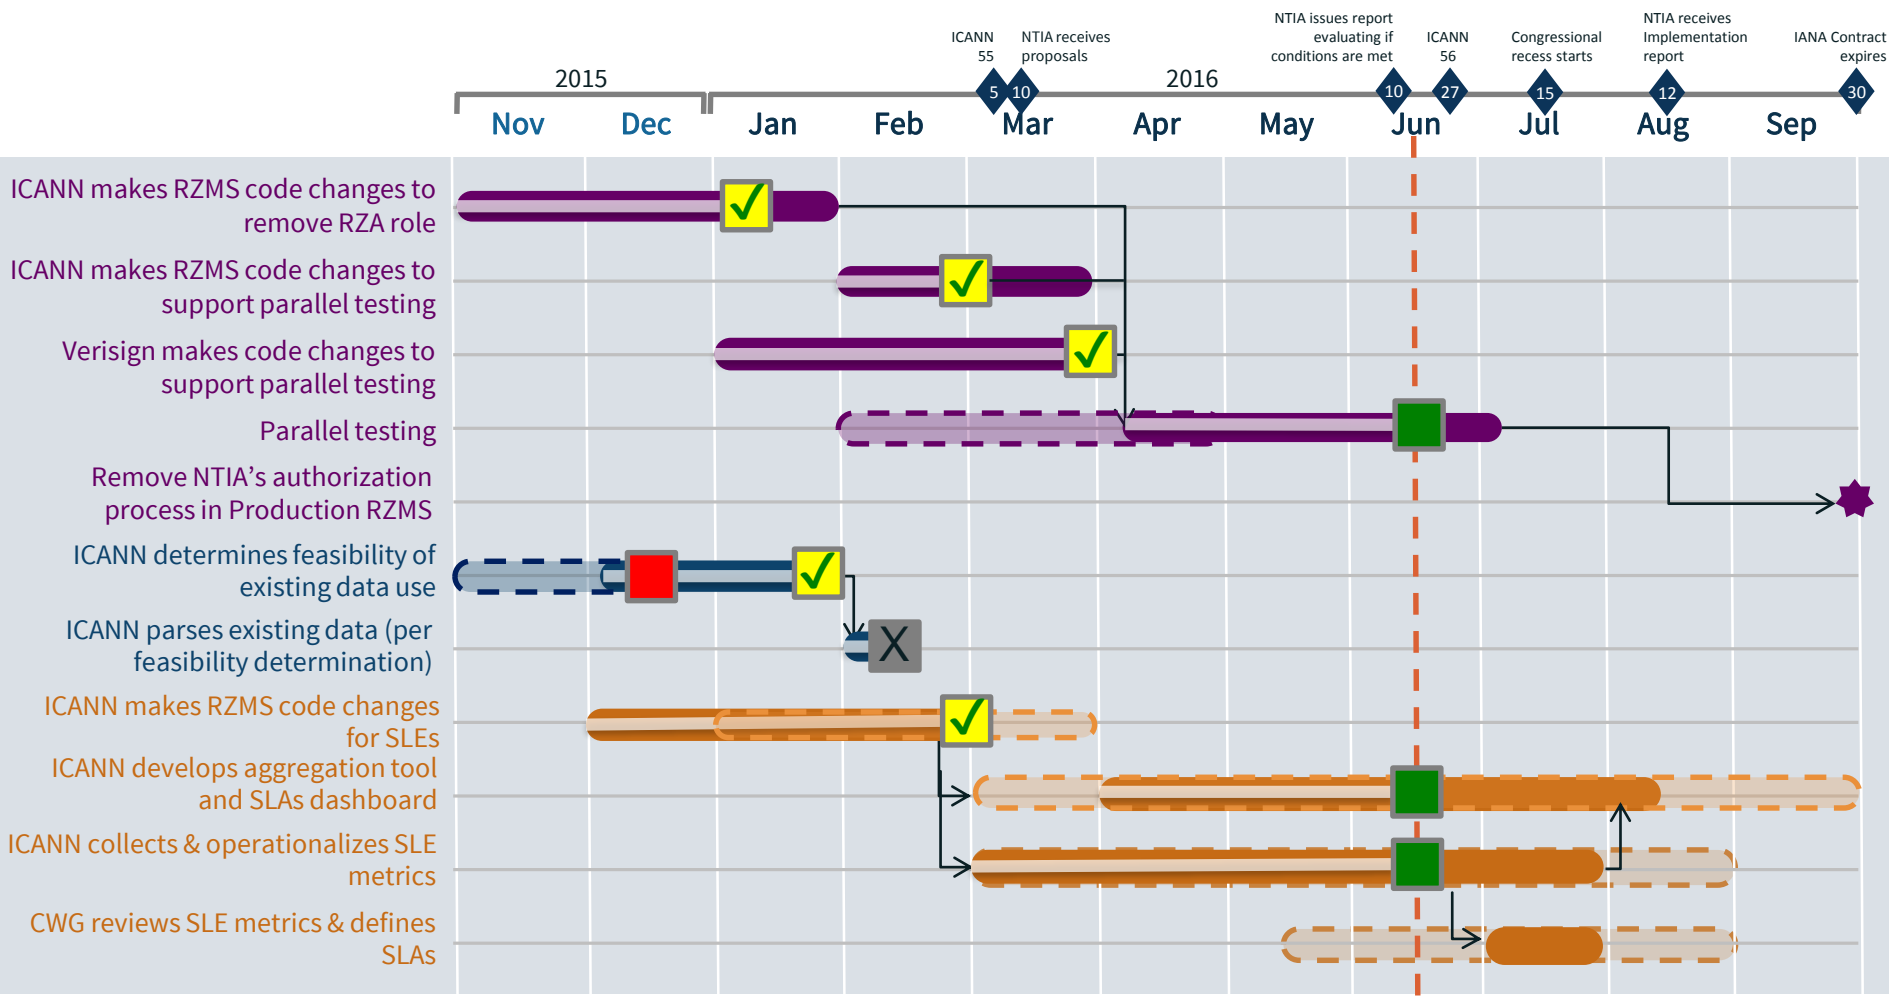

- Project Updates:**
- ✓ Completed 70 days of 90-day Parallel Testing period with no issues.
 - ✓ Collected 3 months of SLE data collection.
 - ✓ Continuing to work on the reporting dashboard.

- Upcoming Activities:**
- Continue to monitor parallel operations.
 - Finalize development of data aggregation tool / reporting dashboard.
 - Elaborate proposal for SLAs thresholds.

Open Items:

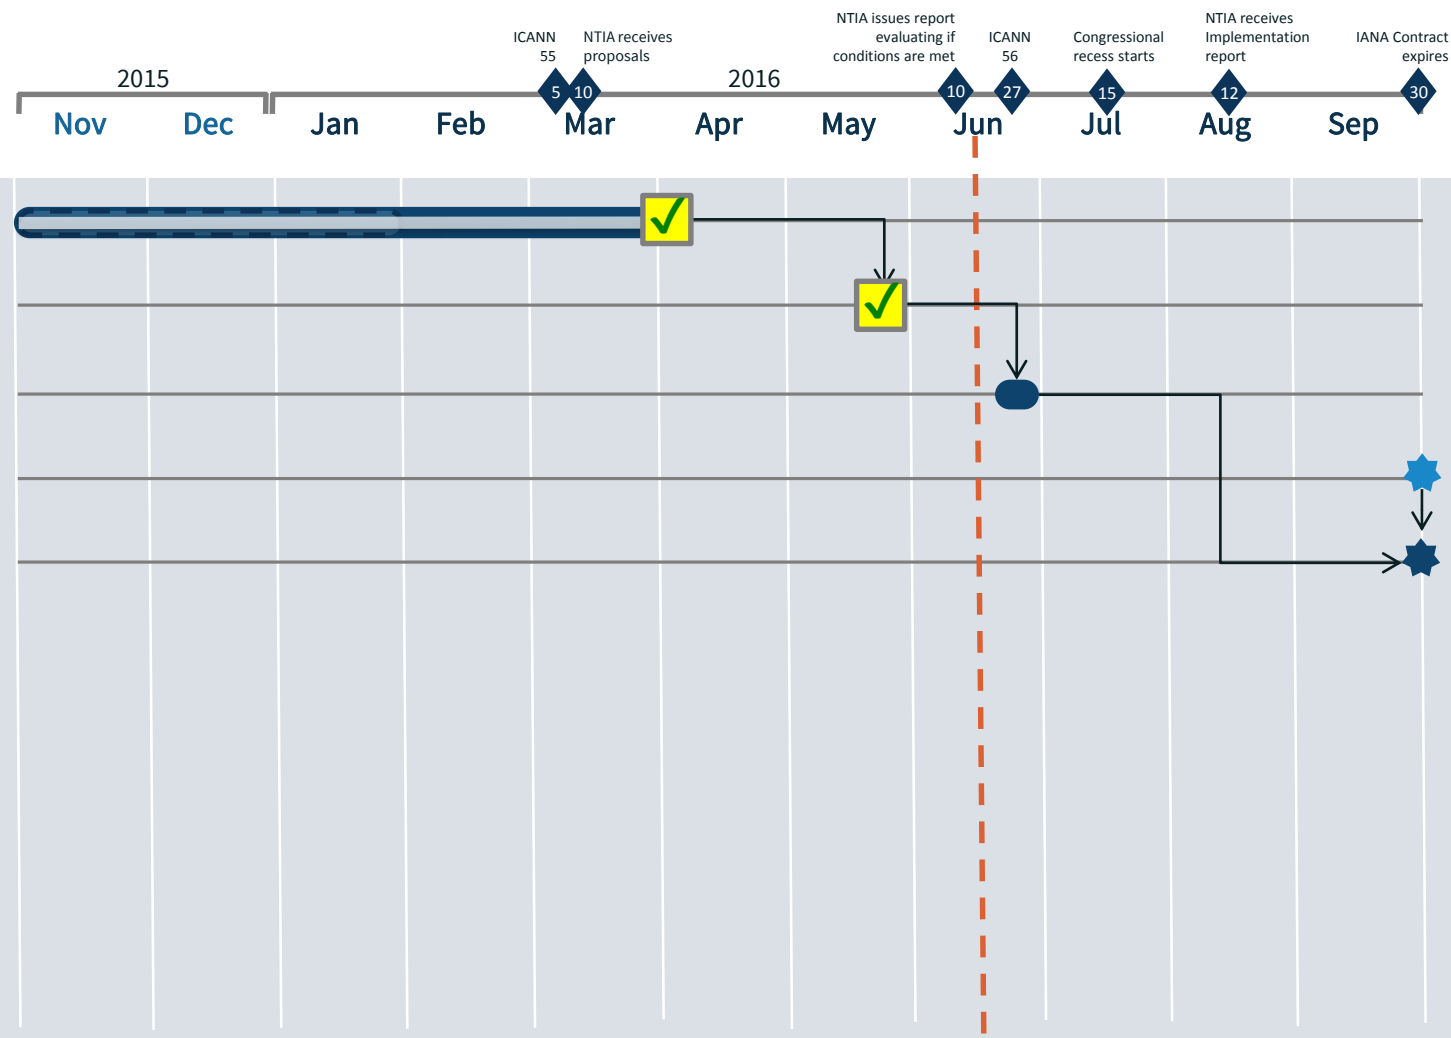


Project Updates:

Upcoming Activities:

- Signing of the RIR SLA document.

Open Items:

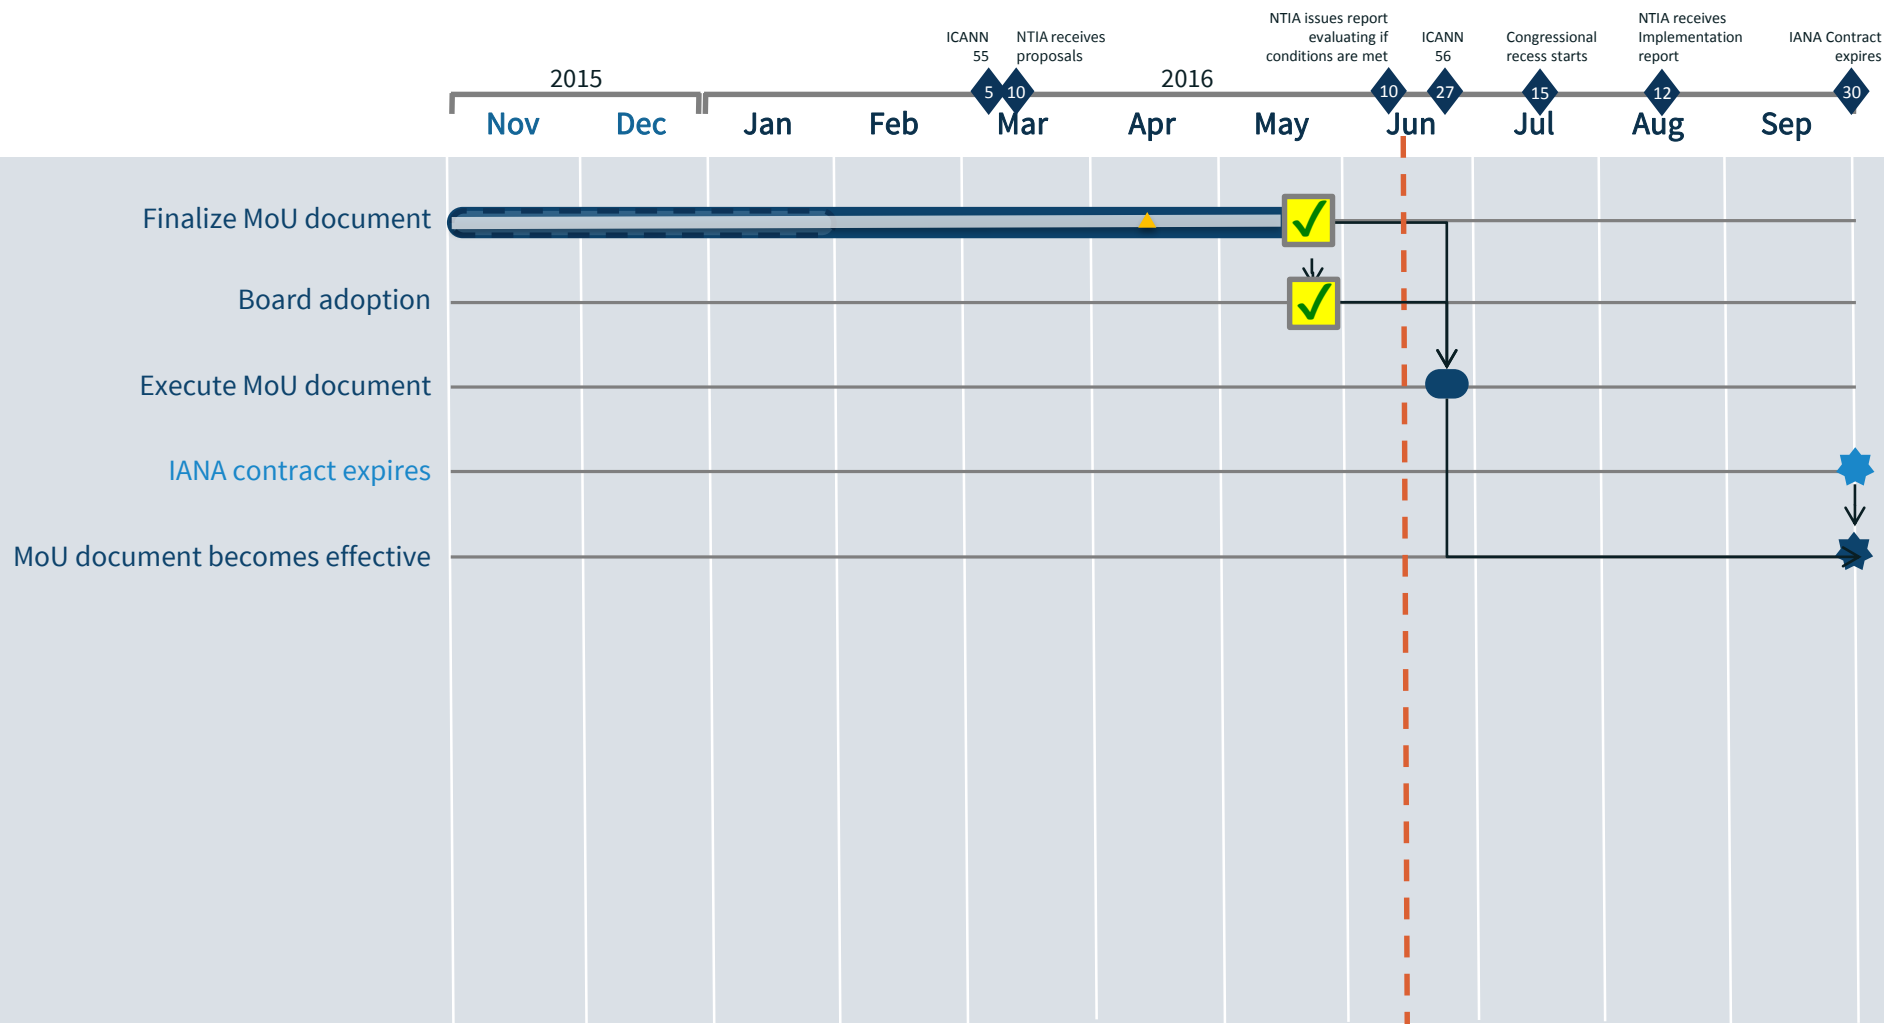

Project Updates:
✓

Upcoming Activities:

- Signing of the IETF MoU document.

Open Items:




DRAFT for Discussion

--- Baseline
 — Current Plan

■ MoU activities
 ■ USG activity

* Timeframes are estimates | 14

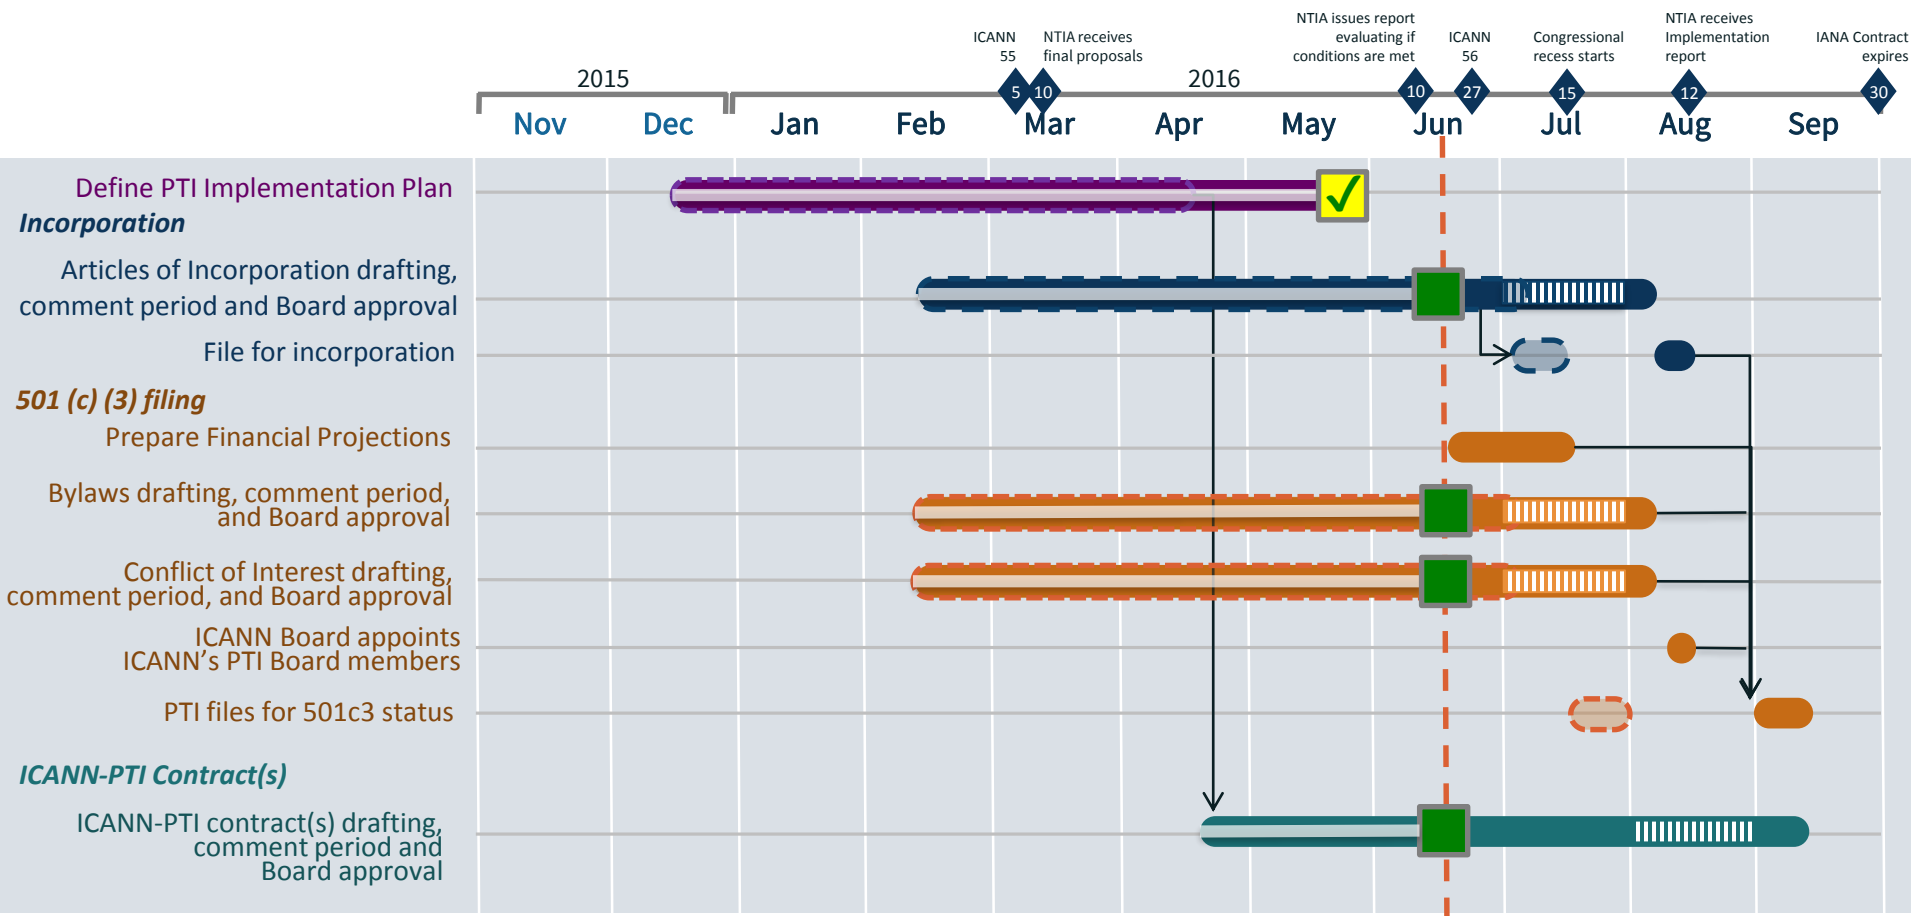


¹ Dependency on performance targets being defined by mid-July 2016 under Names SLEs project to finalize Names contract

Project Updates:
 ✓ Shared PTI staffing rationale with the community.

- Upcoming Activities:**
- Finalize PTI Bylaws and articles of incorporation with the community.
 - Share draft of Naming function contract with the community.

Open Items:

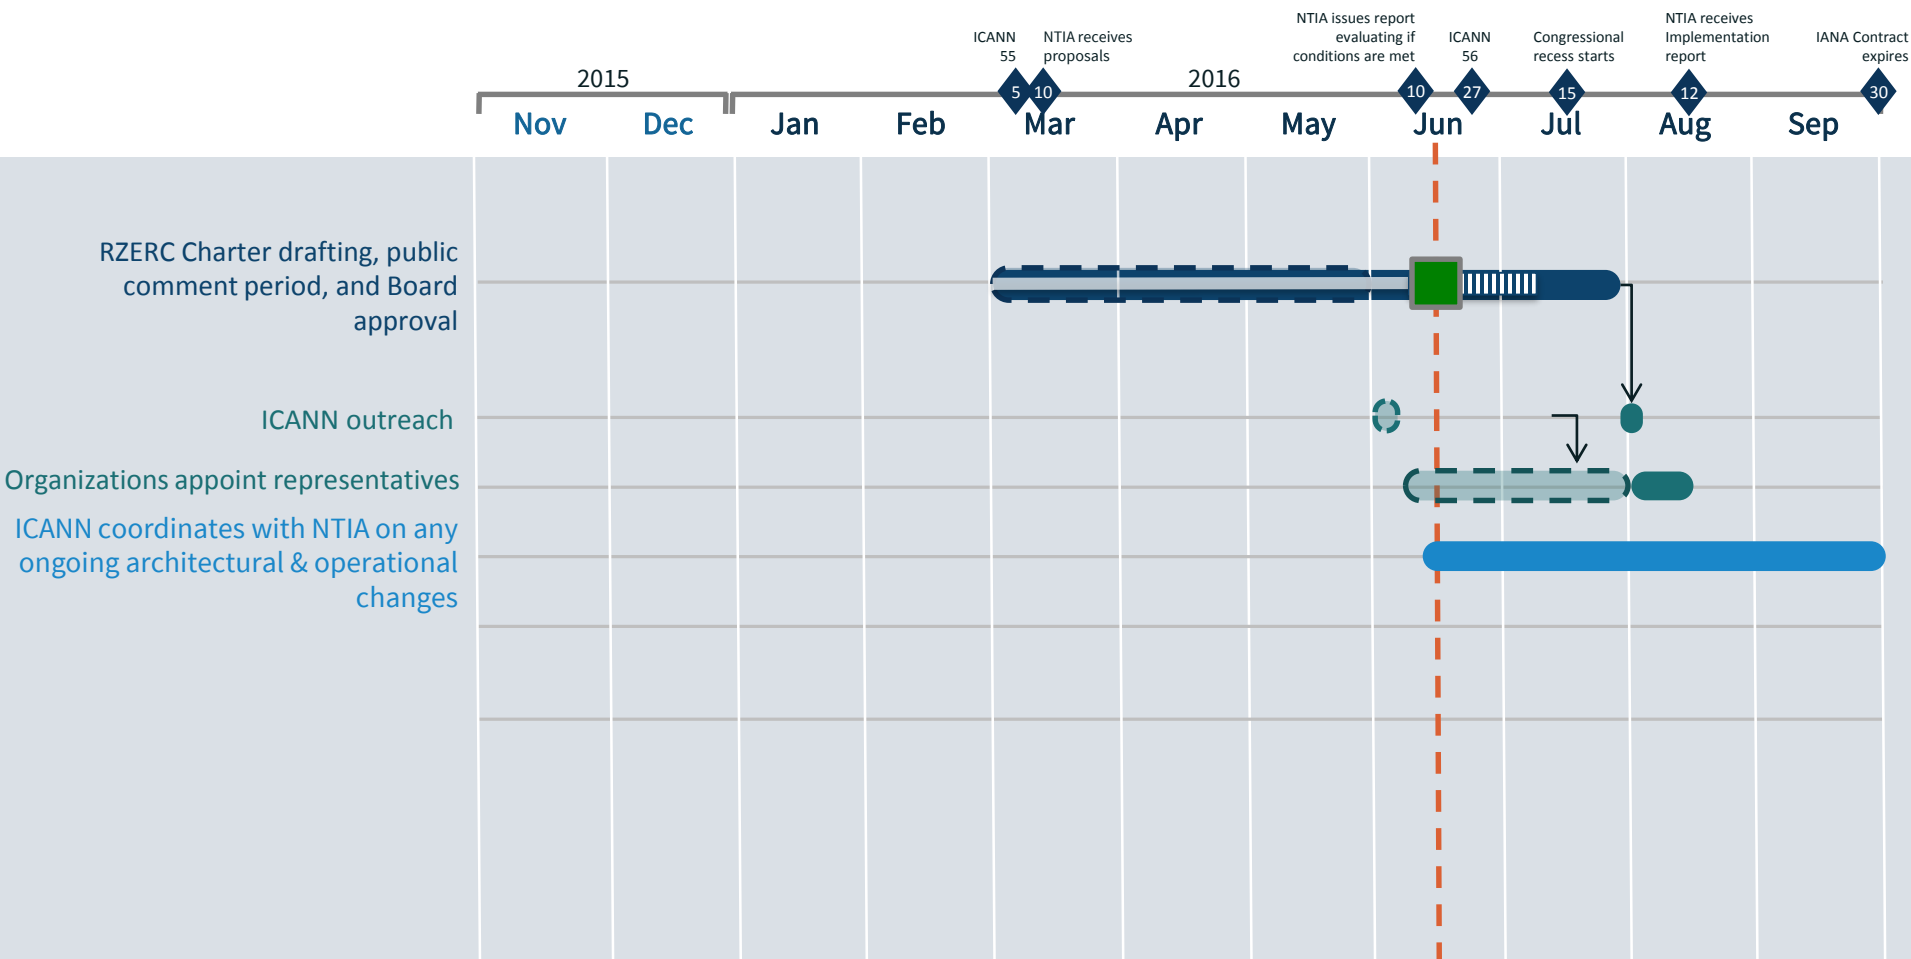


Project Updates:

- ✓ RZERC charter finalized and posted for public comments.


Upcoming Activities:

- Monitor public comments.

Open Items:



CSC Formation

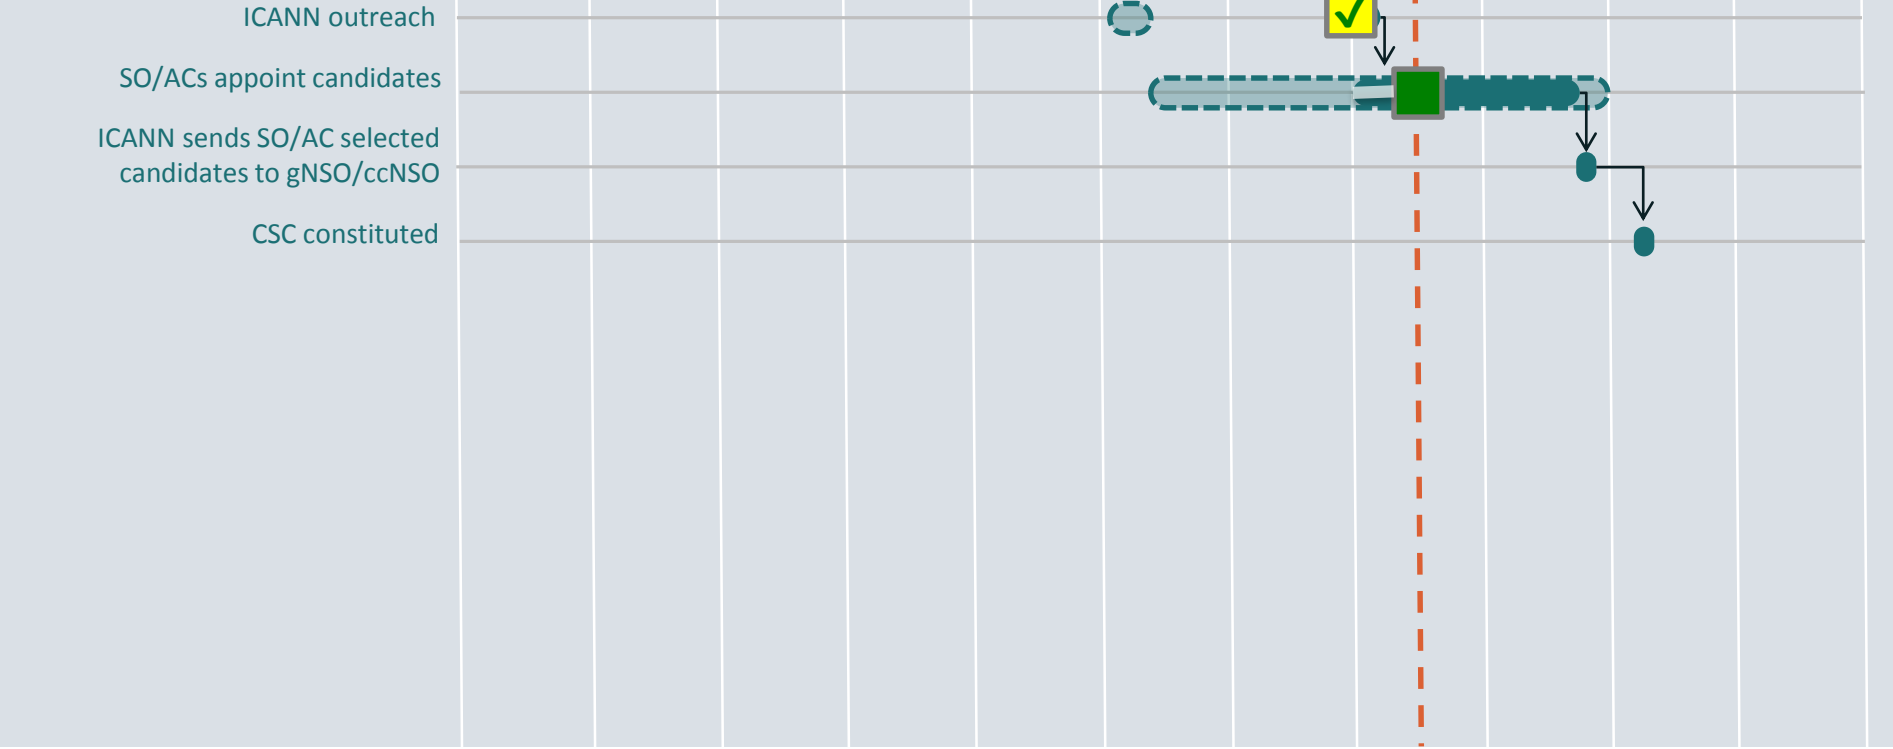


Project Updates:

Upcoming Activities:

- SO/Acs to appoint candidates.

Open Items:

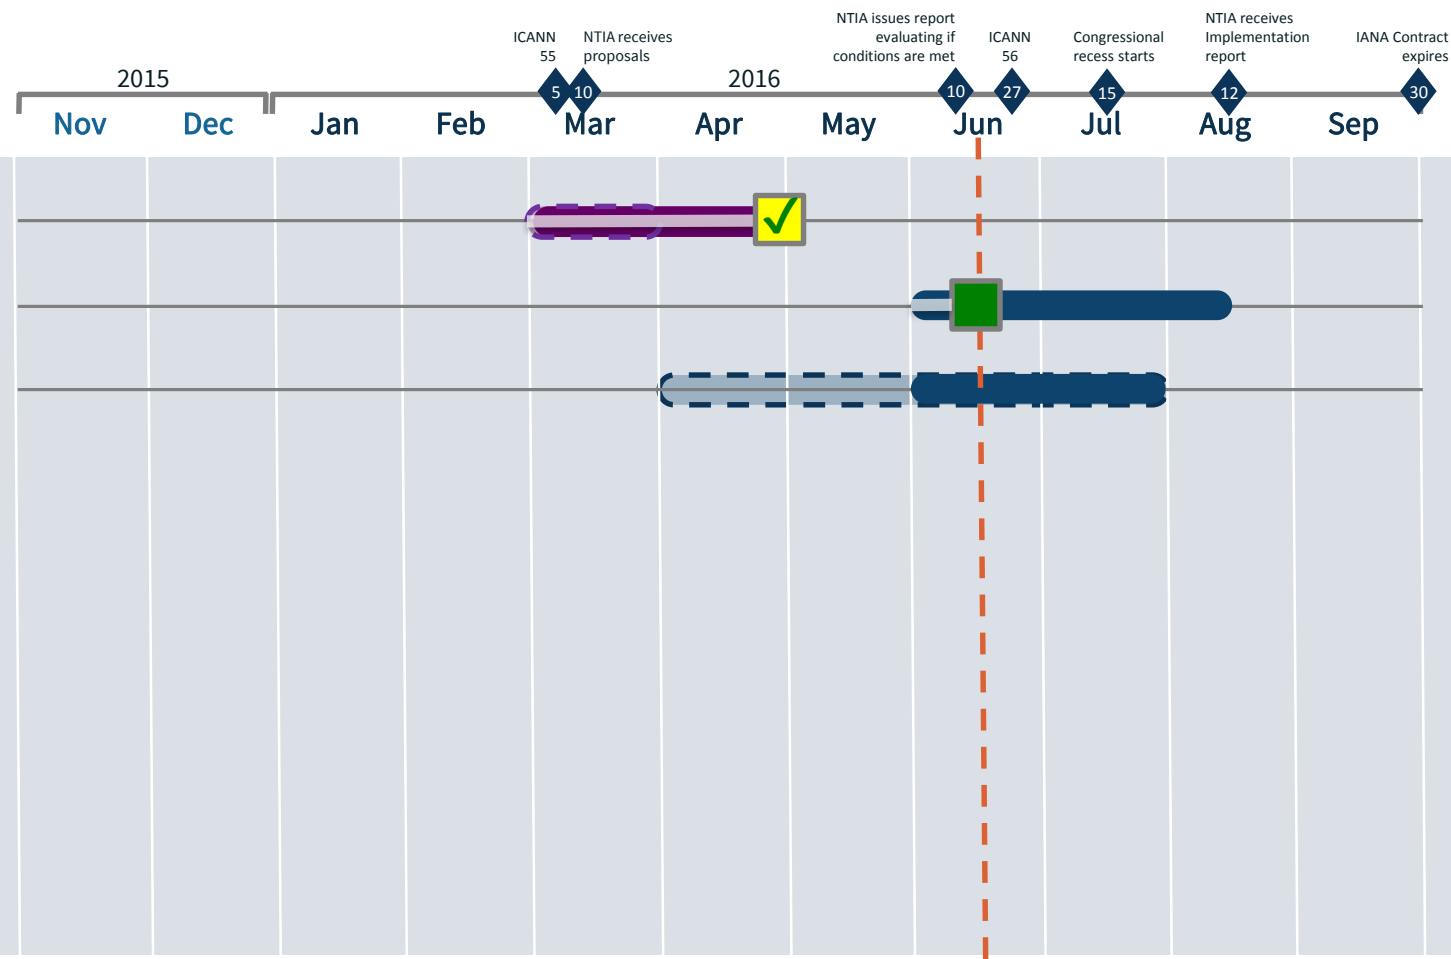


Project Updates:

- ✓ Escalation processes documentation has been updated, and is under management review.

Upcoming Activities:

- Review escalation processes documentation.


Open Items:

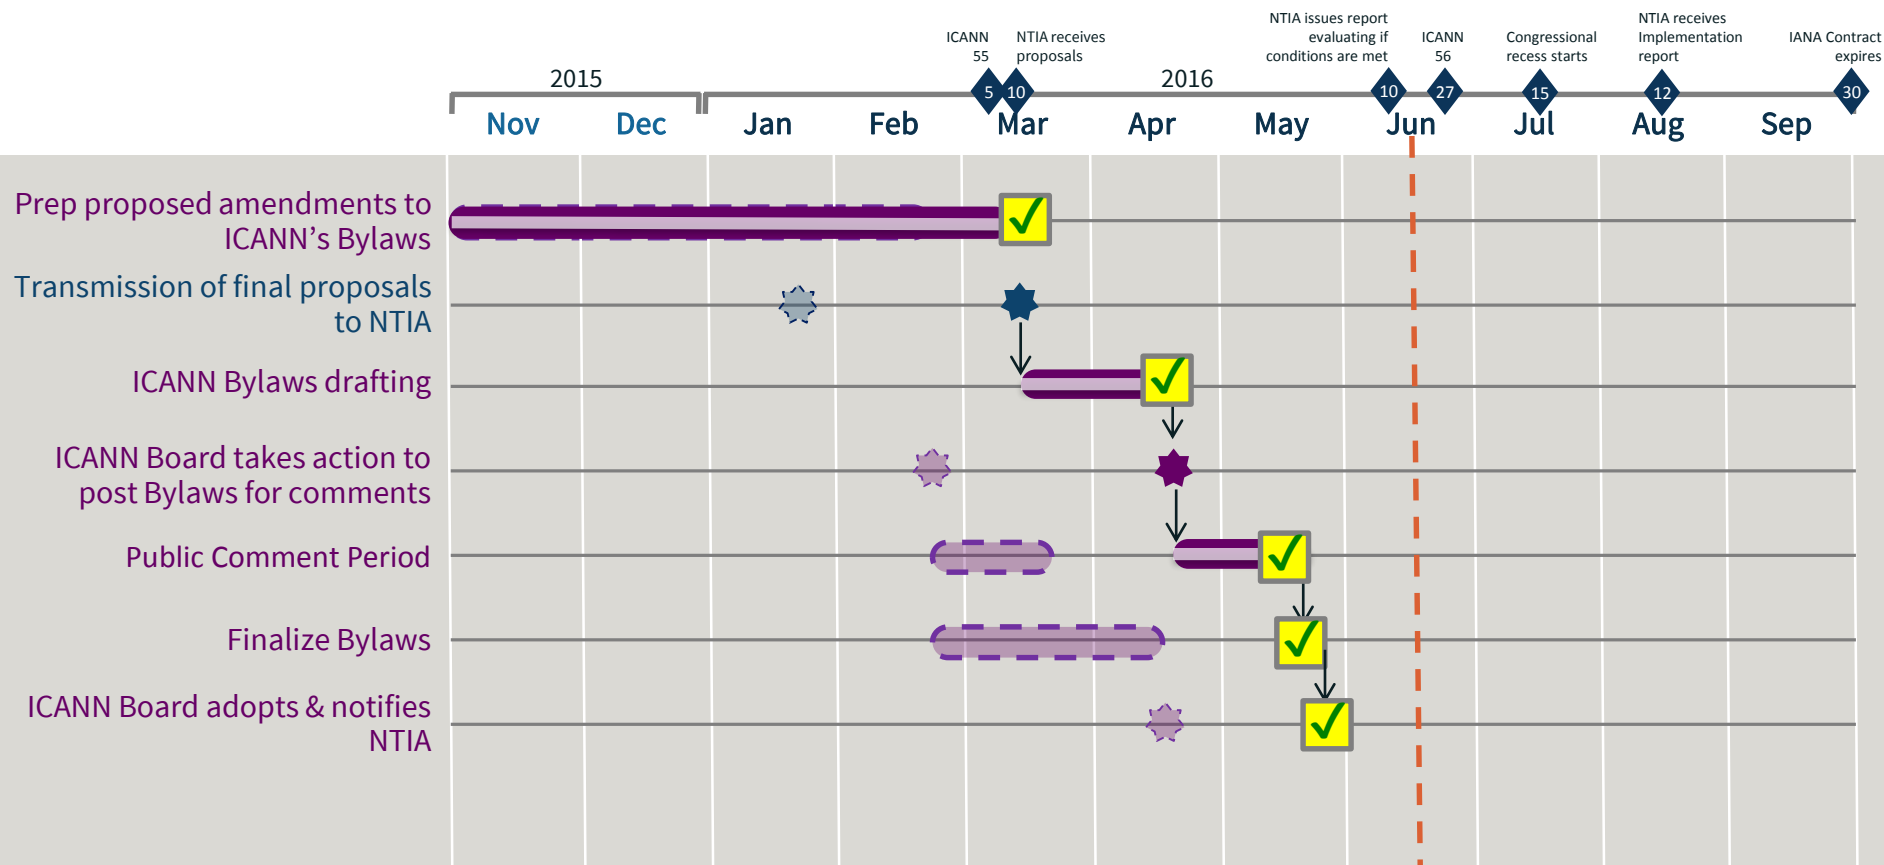

Project Updates:

Upcoming Activities:

Open Items:

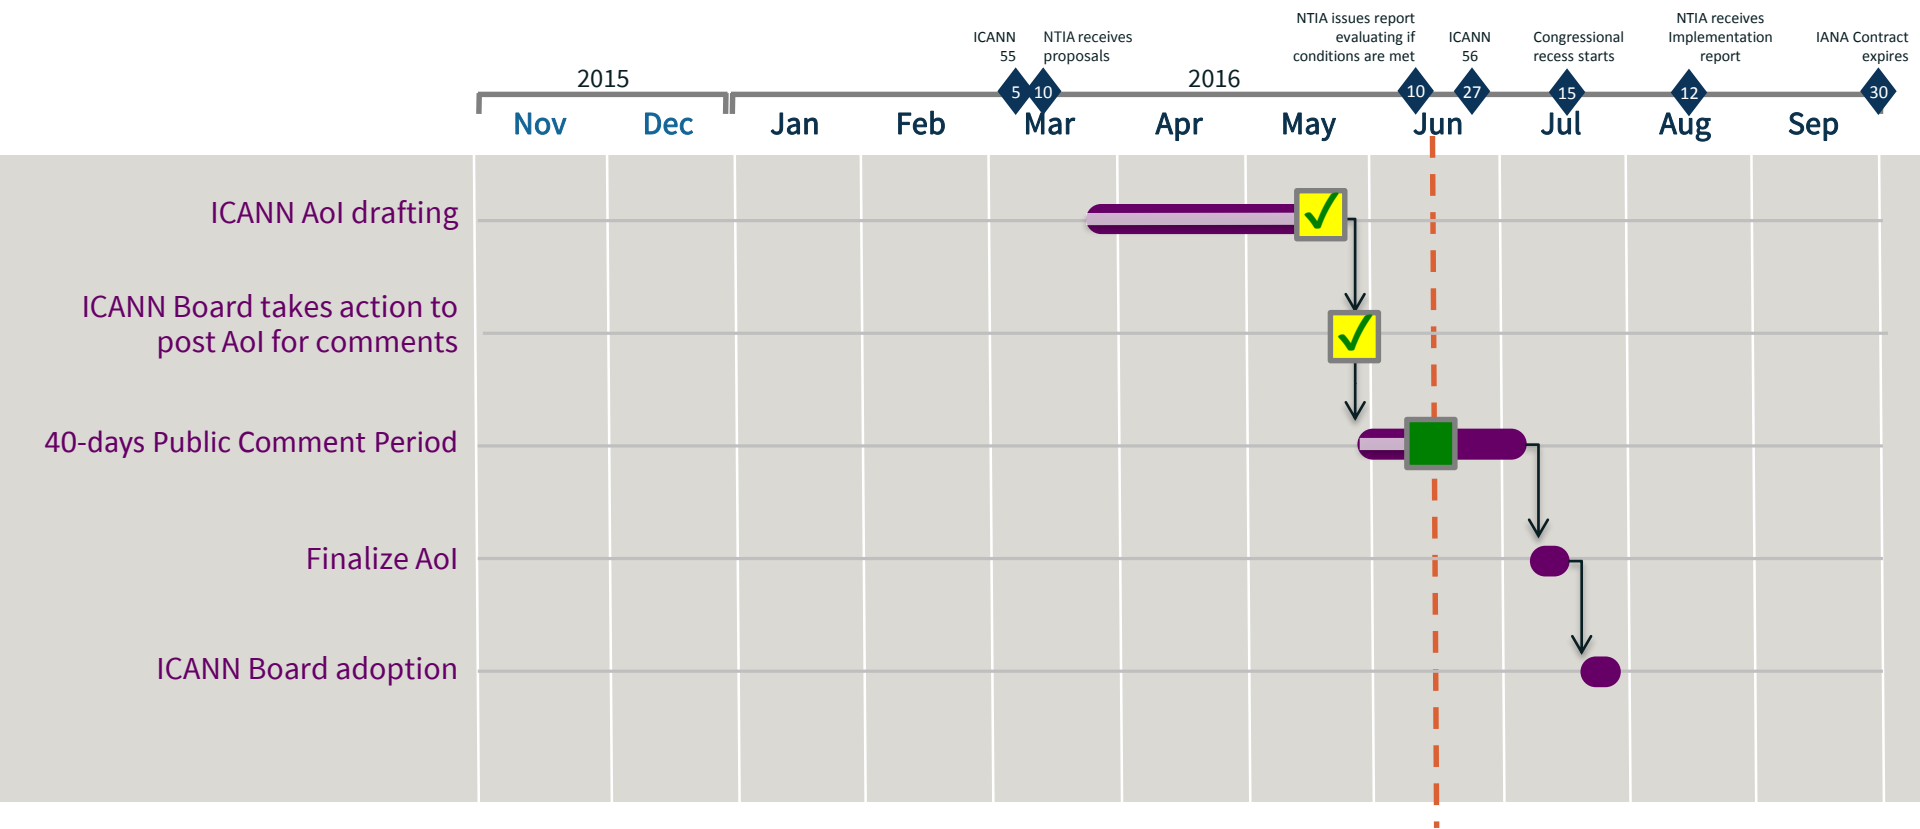

Project Updates:
 ✓ ICANN Articles of Incorporation posted for 40-day Public Comment period.

Upcoming Activities:


- Monitor public comments.

Open Items:

Request For Reconsideration (RR) Enhancements

% Complete: 5%

Status: On-track

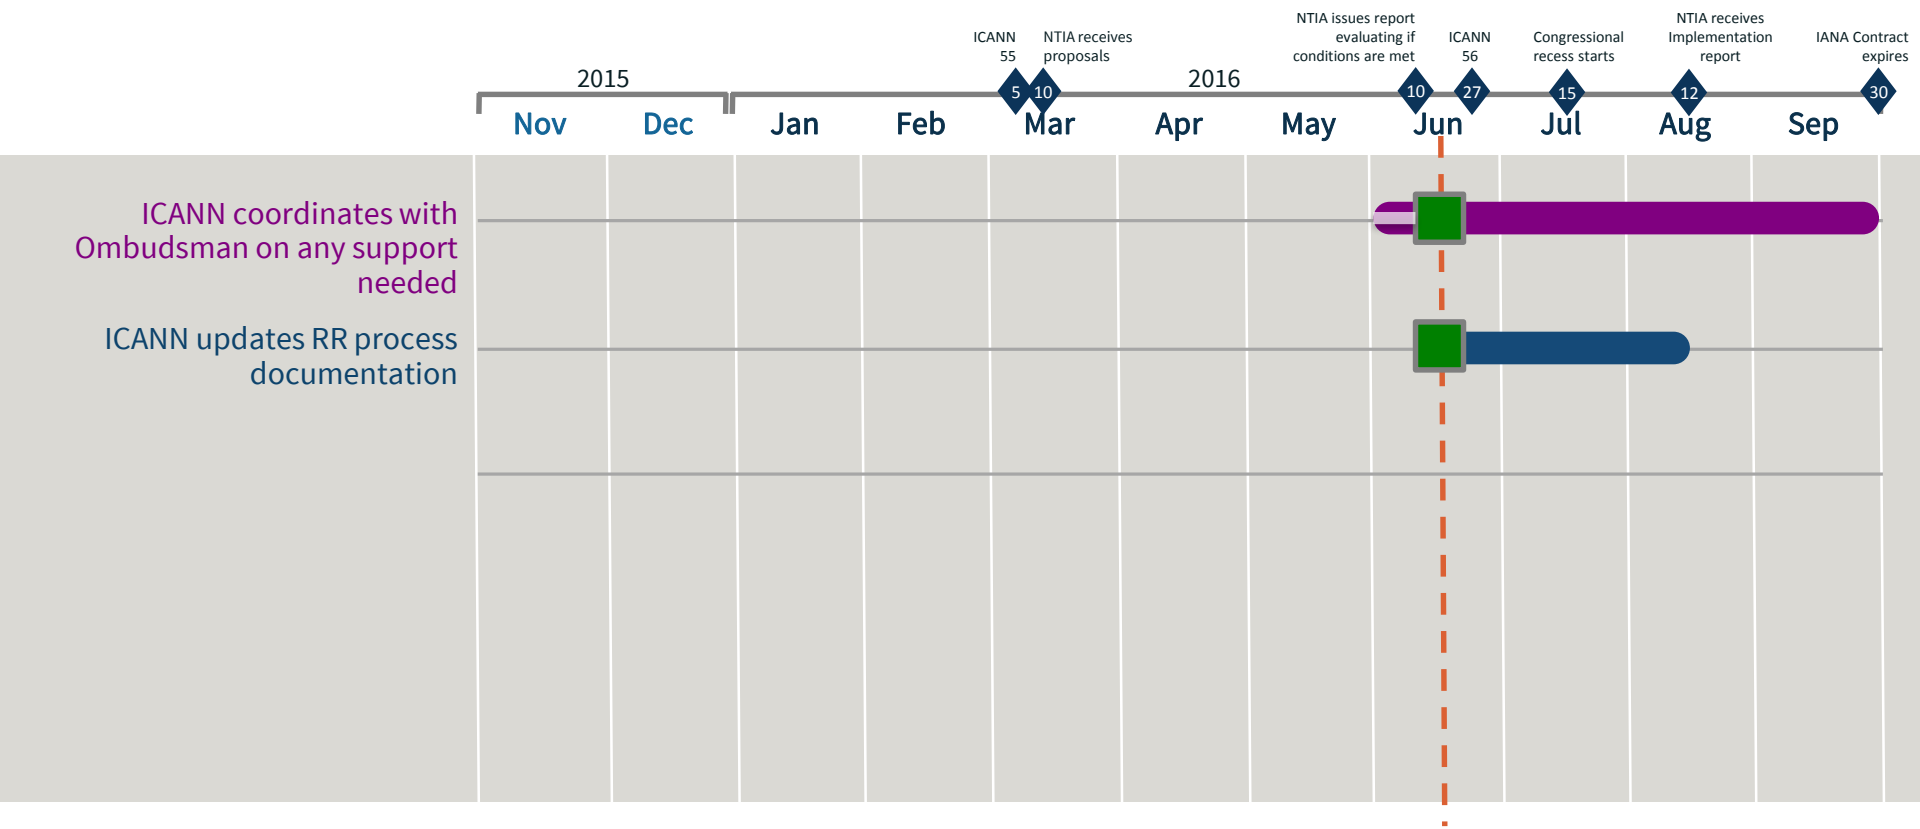

ICANN coordinates with Ombudsman on any support needed

ICANN updates RR process documentation

Project Updates:

Upcoming Activities:

- Update Request for Reconsideration process documentation.

Open Items:




DRAFT for Discussion

--- Baseline
 — Current Plan

■ RR activities

* Timeframes are estimates | 21

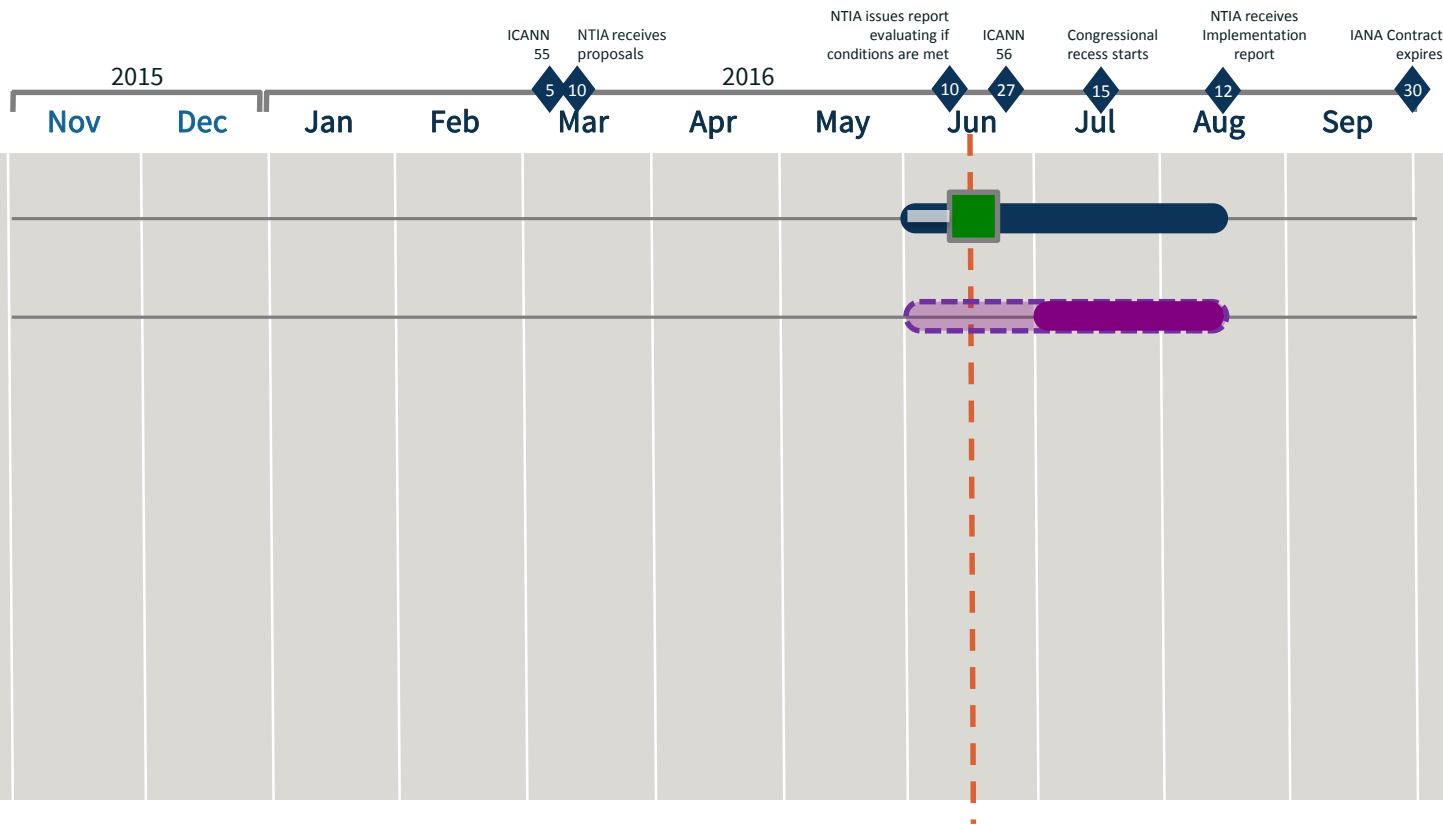

ICANN puts in place mechanisms to support the EC processes

ICANN puts in place secretariat support

Project Updates:

- Started initial assessment of items needed to support the Empowered Community.


Upcoming Activities:

Open Items:

Post-transition Financial Planning Process

% Complete:  50%

Status: On-track

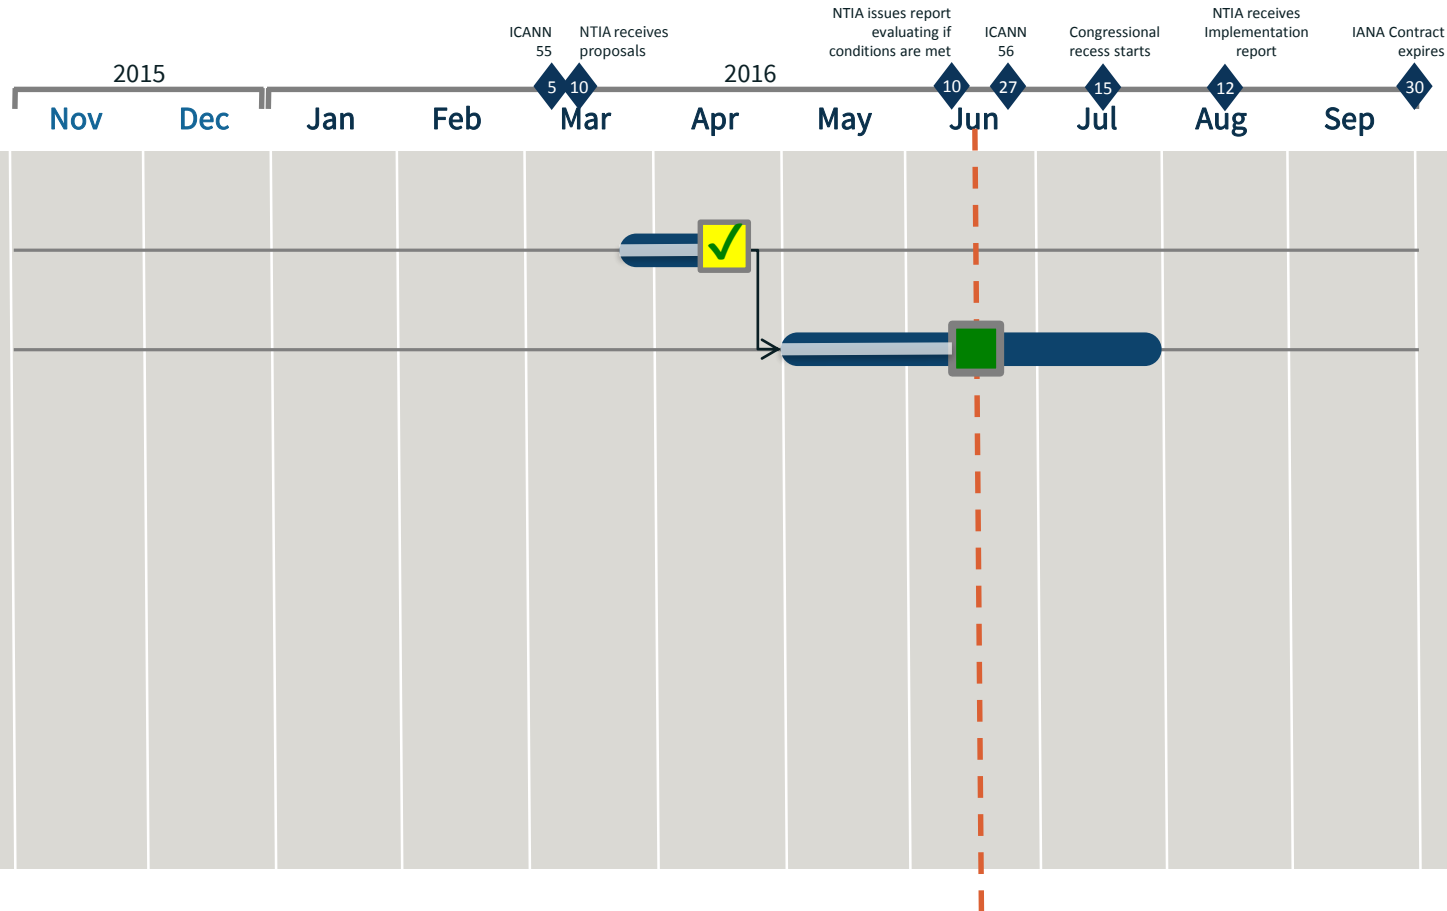

Project Updates:

Upcoming Activities:

- Finalize financial process.

Open Items:



DRAFT for Discussion

--- Baseline
 — Current Plan

* Timeframes are estimates | 23
