




Transition Implementation Status Reporting

08 July 2016

1. Overall Timeline
2. Status Update
3. Appendix: Projects Plans

Overall Timeline

Implementation Planning Timeline – Proposals Delivered in March 2016

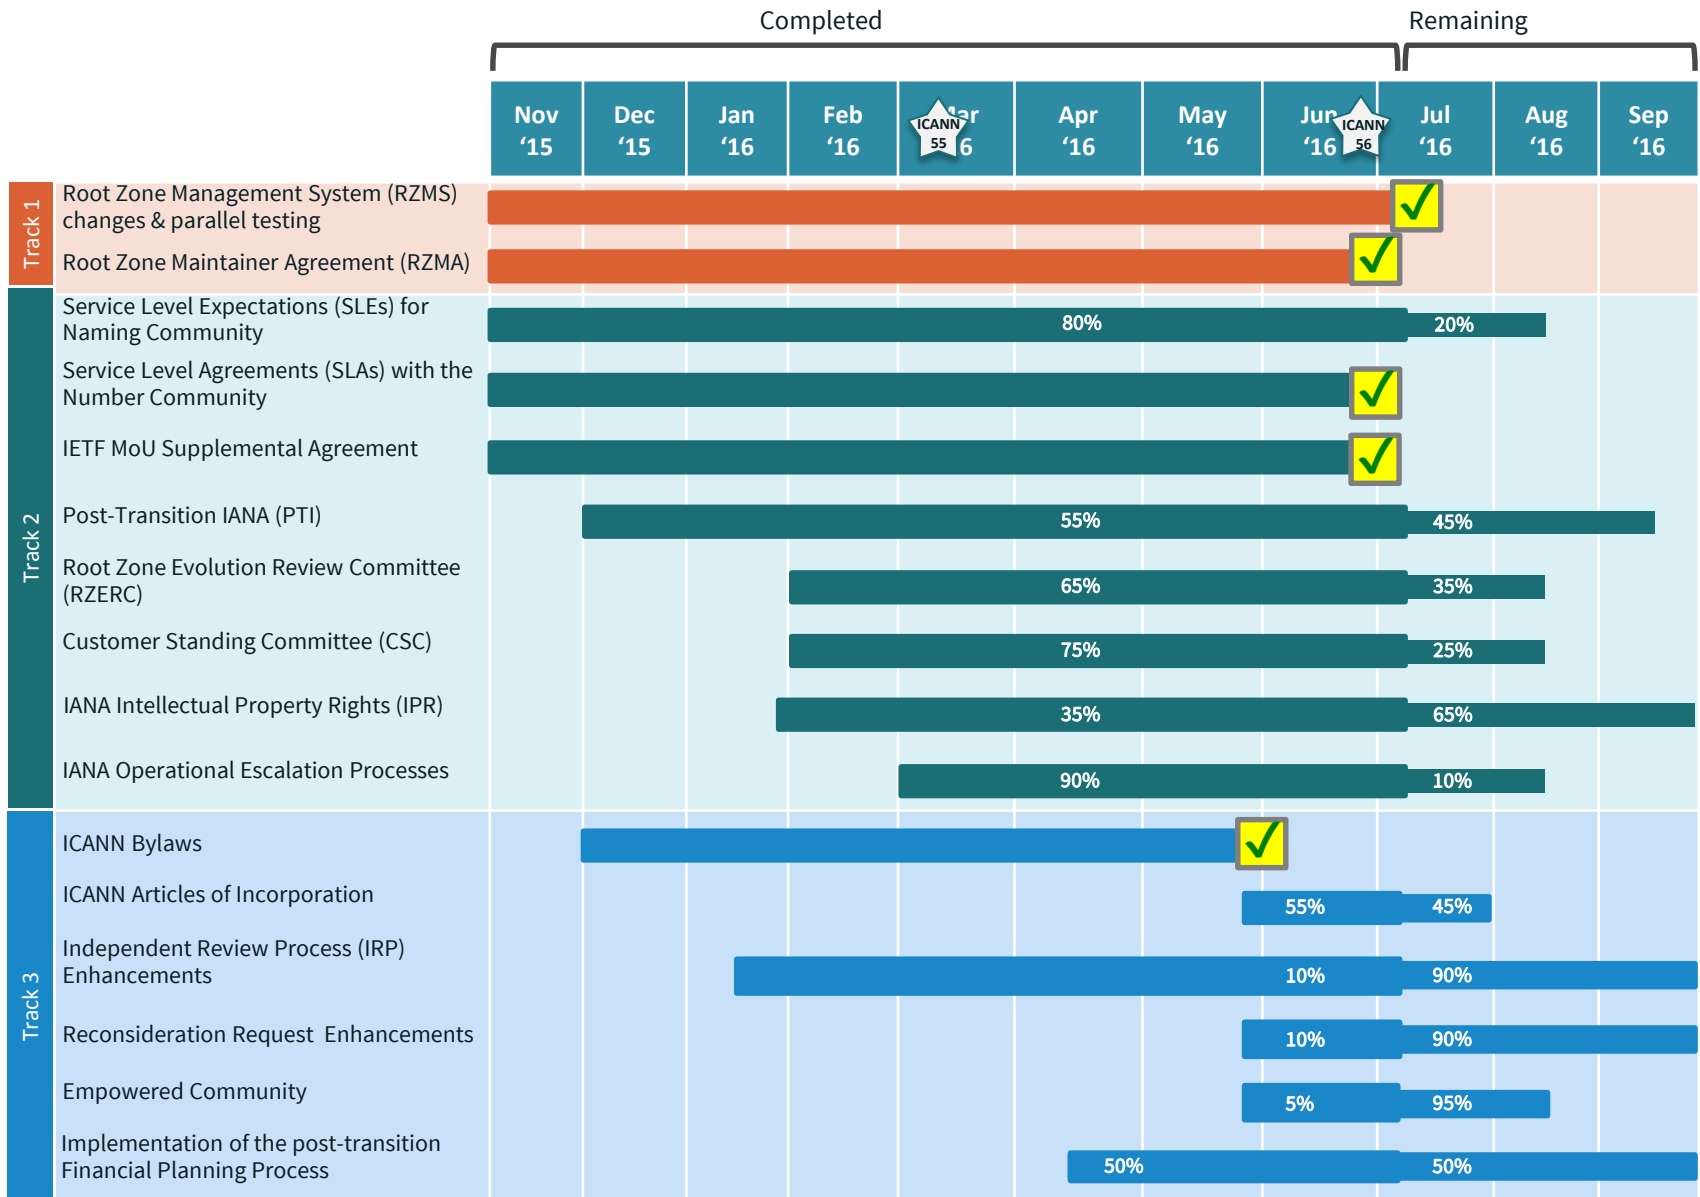

Overall % Complete

64%

Status Update


RZMS, RZMA & Names SLEs

Status As Of Date:

07/08/16

Project	Description	Plan Completion Date	Status	% Complete
RZMS changes to remove RZA role and support parallel testing	Remove NTIA's authorization process from RZMS (code changes for ICANN and Verisign, and parallel testing).	09/30/16 08/15/16 07/06/16		100%
Names SLEs (SLEs for Naming Community)	RZMS code changes to accommodate new SLEs, inclusion of performance targets in ICANN-PTI contract, dashboard reporting of SLAs.	09/30/16 08/15/16		80%
RZMA (Agreement with Root Zone Maintainer)	Completion of draft RZMA.	01/31/16 / 02/29/16 04/15/16 / 04/30/16 05/15/16 / 05/31/16/ 06/30/16		100%

Key Dates:

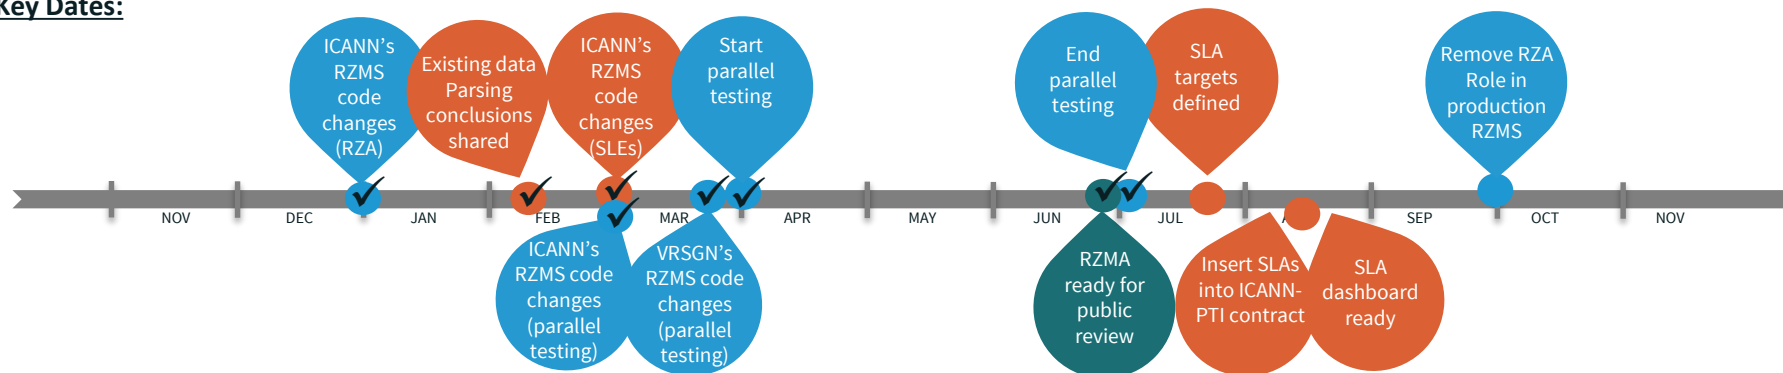

Project Updates:

- ✓ Completed 90-day Parallel Testing period with no unexplained issues.
- ✓ Finalizing SLE performance targets proposal.
- ✓ Continuing to work on the reporting dashboard.
- ✓ Finalized RZMA.

Upcoming Activities:

- Continue to fine-tune dashboard.
- Share proposed Names performance targets with the community.

Open Items:



DRAFT for Discussion

- On-track
- Behind schedule, but recovery still possible





- Not started
- Target will be missed

* All dates are estimates | 6

RIRs SLAs & IETF MoU Supplemental Agreement


Status As Of Date:

07/08/16

Project	Description	Plan Completion Date*	Status	% Complete
RIRs SLAs (Service Level Agreement with the Number Community)	Completion of draft agreement, including SLAs with RIRs, and operationalization of SLAs.	06/30/16		 100%
IETF MoU Supplemental Agreement	Completion of draft ICANN-IETF MoU Supplemental Agreement.	06/30/16		 100%

* Completion Date dependent on USG's approval of proposals

Key Dates:

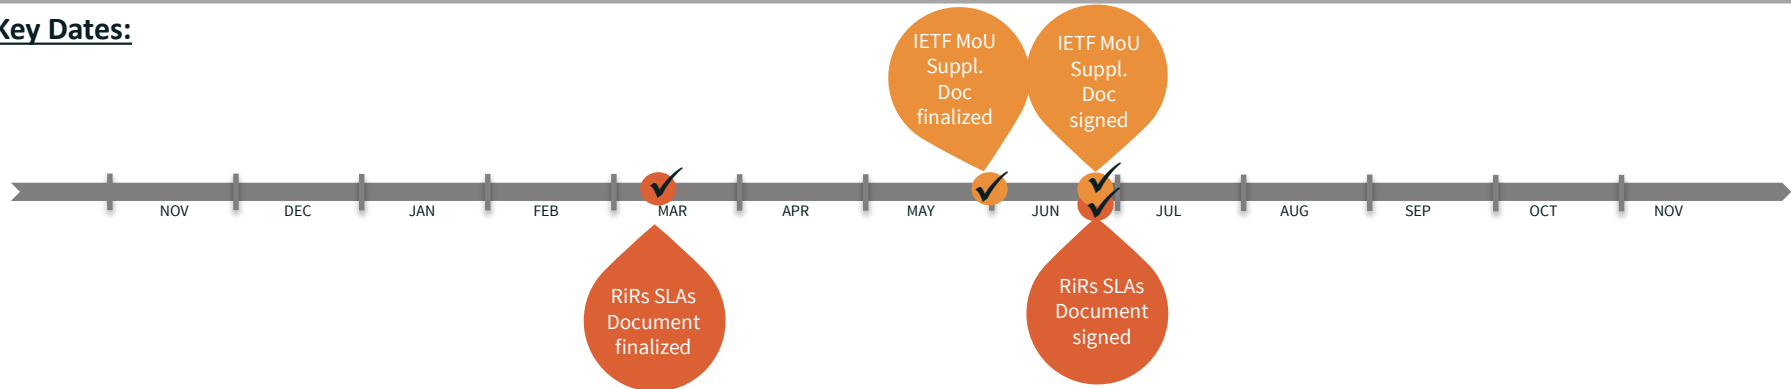

Project Updates:

- RIR SLA document signed.
- IETF MoU document signed.

Upcoming activities:

Open Items:



DRAFT for Discussion



On-track



Behind schedule, but recovery still possible



Not started




Target will be missed

* All dates are estimates

Project	Description	Plan Completion Date	Status	% Complete
PTI <i>(Post-Transition IANA)</i>	Formation of PTI entity: legal formation (incorporation of affiliate, filing for 501c3, drafting of contract, etc.) and operationalization of PTI entity (board nominations, budget, etc.).	09/30/16 08/15/16 09/30/16		55%

Key Dates:

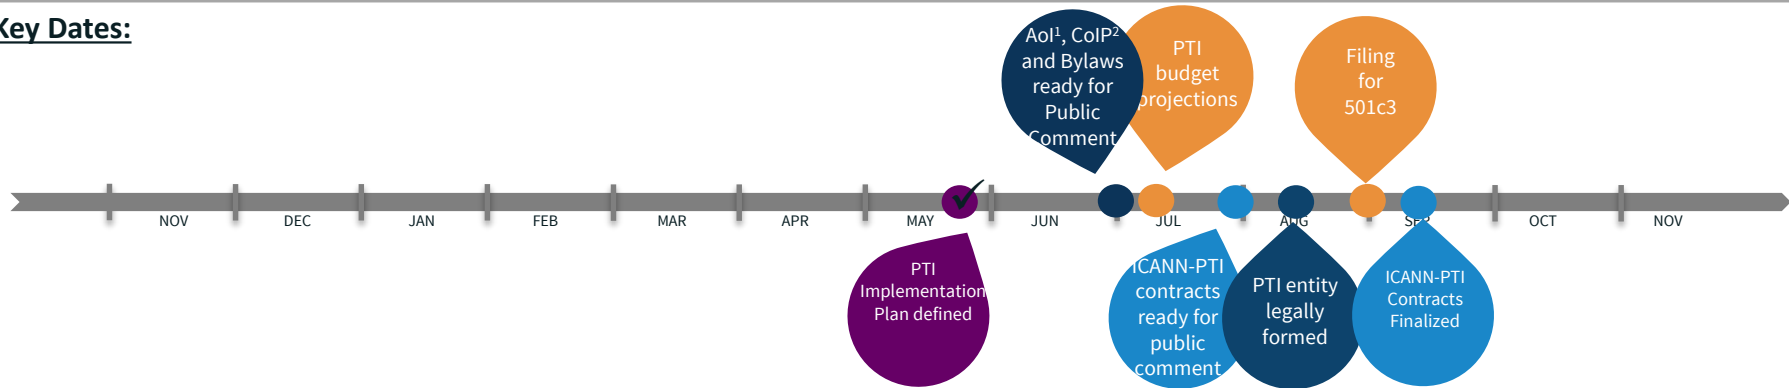

¹ Aol: Articles of Incorporation / ²CoIP: Conflicts of Interest Policy

Project Updates:

- ✓ PTI articles of incorporation, conflict of interest policy, code of conduct and expected standard of behavior posted for 30-day public comment period.

Upcoming activities:

- Finalize PTI Bylaws for public comment posting.
- Share draft of Naming function contract with the community.

Open Items:


IPR, RZERC, CSC & Escalation Processes

Status As Of Date:

07/08/16

Project	Description	Plan Completion Date	Status	% Complete
IANA IPR	Transfer of IANA IPR to a independent trust.	9/30/16		35%
RZERC (<i>Root Zone Evolution Review Committee</i>)	Formation of committee to advise ICANN Board on RZMS architectural and operational changes.	09/30/16 08/15/16		65%
CSC (<i>Customer Service Standing Committee</i>)	Formation of committee to monitor PTI performance.	09/30/16 08/15/16		75%
Escalation Processes	Updating of existing IANA operational complaint and escalation processes.	09/30/16 08/15/16		90%

Key Dates:

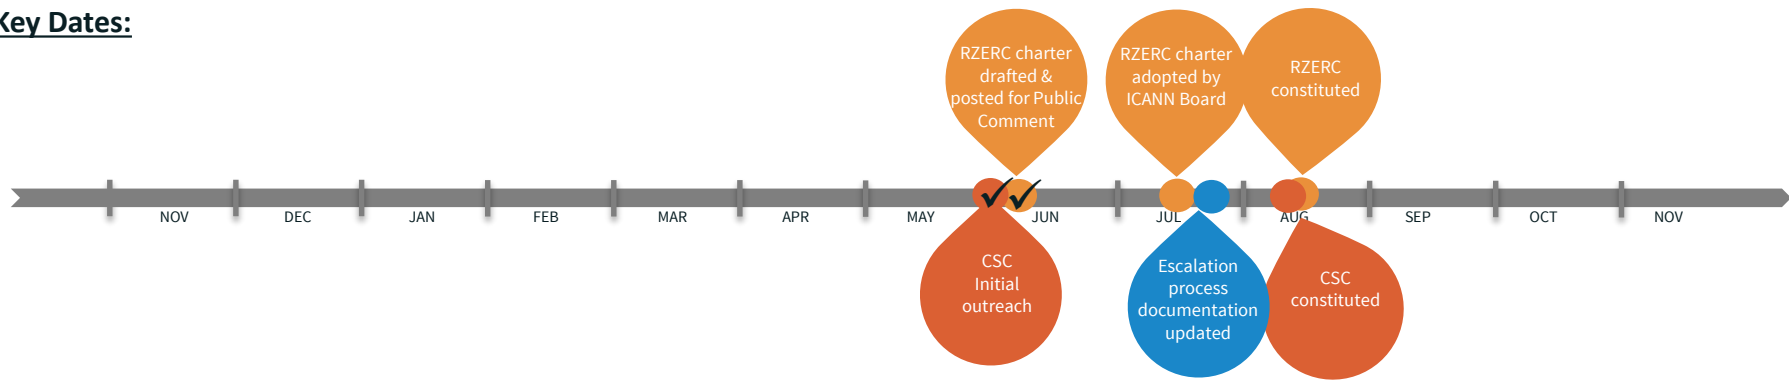

Project Updates:

- ✓ RZERC charter public comment period ends on July 10.
- ✓ Appointing organizations working on appointing candidates.
- ✓ Escalation processes documentation being updated.

Upcoming Activities:

- Analyze public comments on RZERC charter and revise the charter.
- Appointing organizations submit candidates.
- Finalize escalation processes documentation.

Open Items:

- Waiting on implementation requirements for IANA IPR.



DRAFT for Discussion

- On-track
- Behind schedule, but recovery still possible
- Not started
- Target will be missed

* All dates are estimates


Enhancing ICANN's Accountability

Status As Of Date:

07/08/16

Project	Description	Plan Completion Date	Status	% Complete
ICANN's Bylaws	Updating of ICANN Bylaws.	06/09/16 05/27/16		100%
ICANN's Articles of Incorporation (Aol)	Updating of ICANN Articles of Incorporation	07/31/16		55%
IRP Enhancements	Implement enhancements to Independent Review Process.	09/30/16 – 08/15/16 09/30/16		10%
RR Enhancements	Implement enhancements to ICANN's reconsideration request process.	09/30/16 08/15/16		10%
Empowered Community Support Mechanisms	Implement processes and mechanisms in support of the empowered community.	09/30/16 08/15/16		5%
Financial Planning Process Updates	ICANN caretaker budget, PTI caretaker budget and PTI budget.	08/15/16		50%

Key Dates:



Project Updates:

- ✓ Monitoring public comments on ICANN Aol.
- ✓ Started initial assessment of items needed to support the Empowered Community.

Upcoming Activities:

- Analyze public comments and finalize ICANN articles of incorporation.
- Finalize financial planning process.

Open Items:



DRAFT for Discussion



On-track



Behind schedule, but recovery still possible



Not started




Target will be missed

* All dates are estimates | 10



Appendix High-Level Project Plans

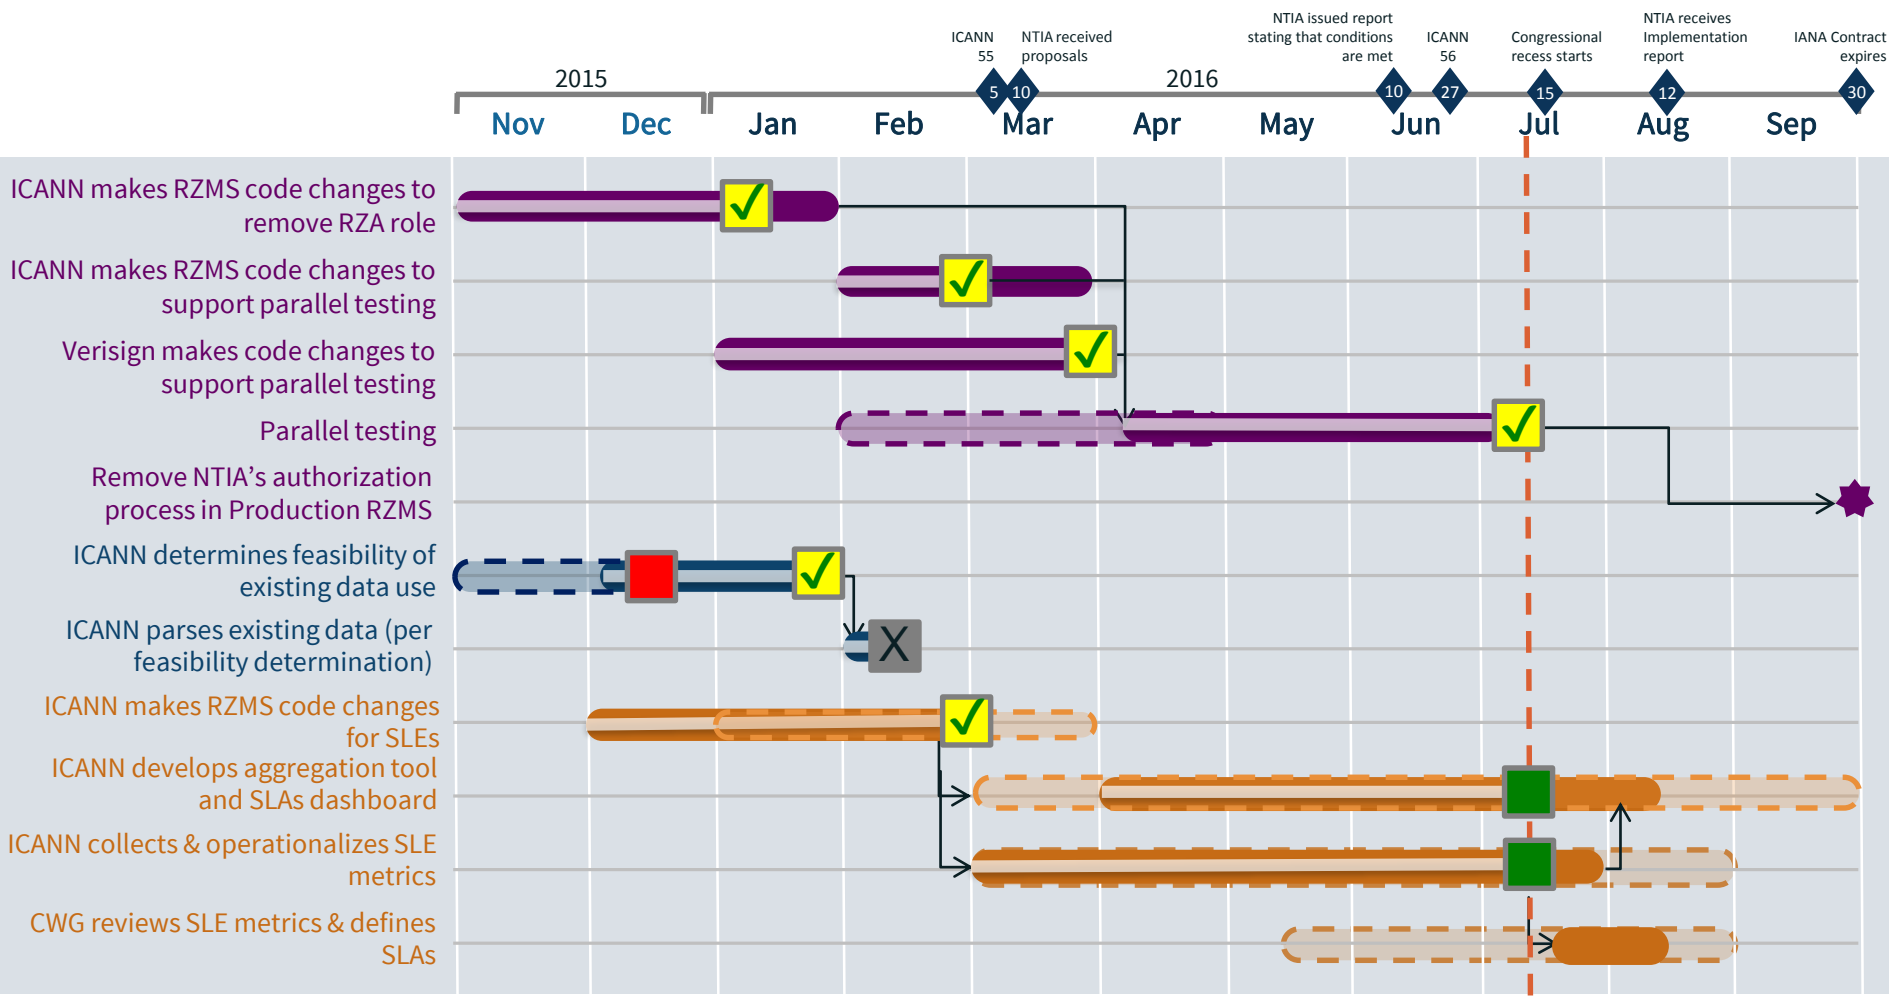


Project Updates:

- ✓ Completed Parallel Testing period with no unexplained issues.
- ✓ Finalizing SLE performance targets proposal.
- ✓ Continuing to work on the reporting dashboard.

Upcoming Activities:

- Continue to fine-tune dashboard.
- Share proposed performance targets with the community.

Open Items:

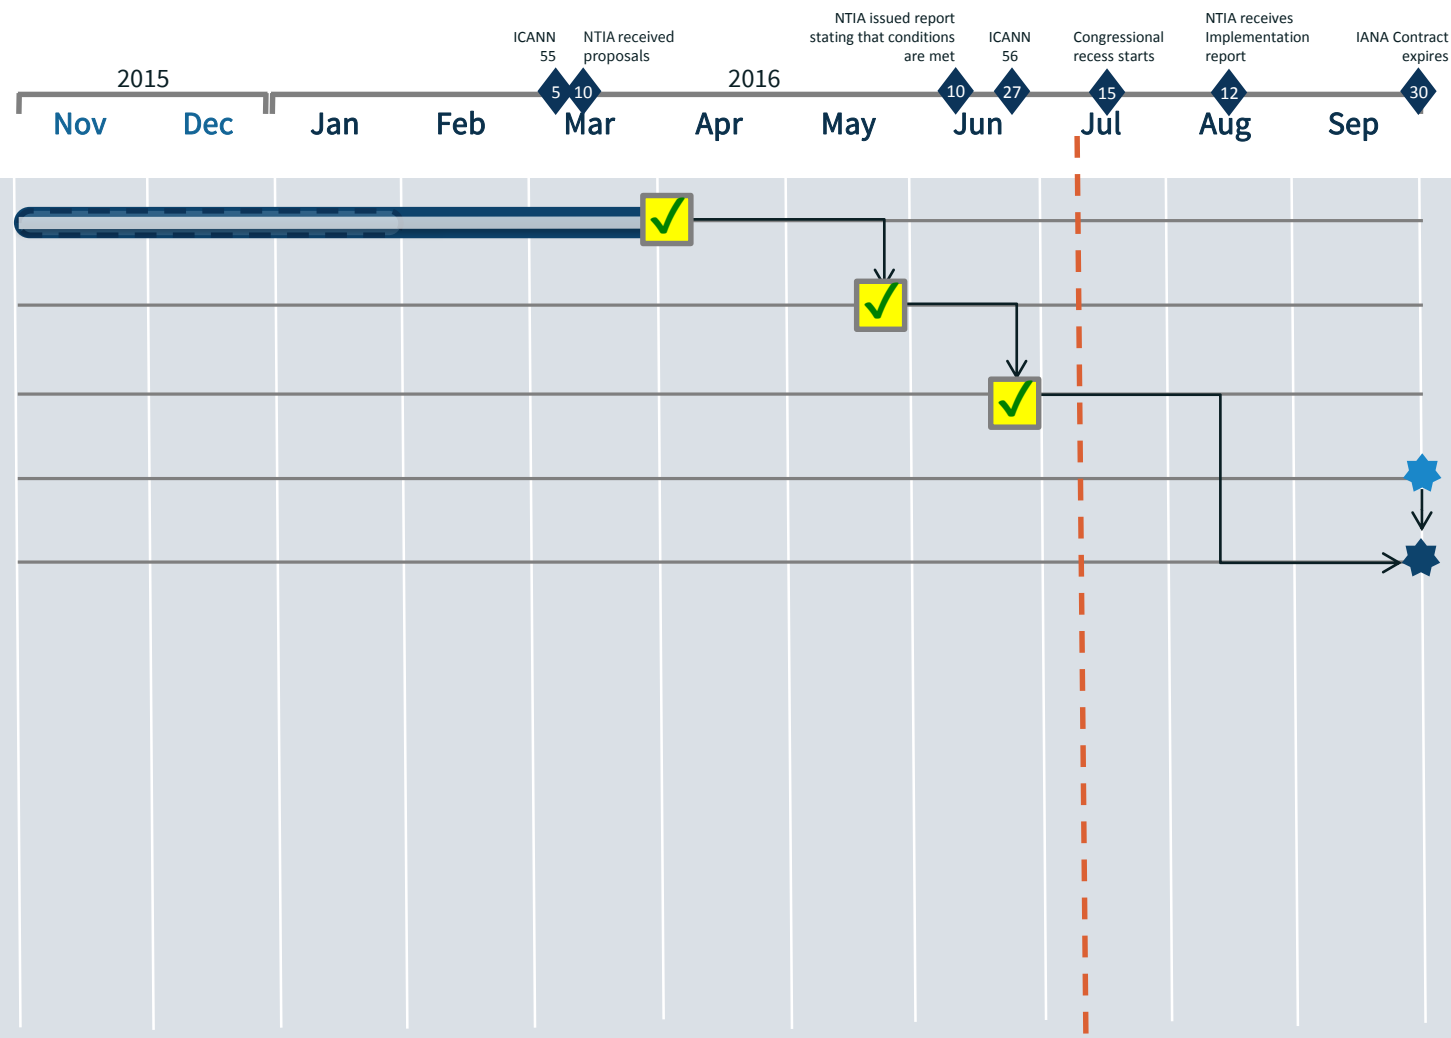

Project Updates:
 ✓ Signed the RIR SLA document.

Upcoming Activities:

Open Items:




DRAFT for Discussion

Baseline
 Current Plan
 RIRs SLAs activities
 USG activity

* Timeframes are estimates | 13

IETF MoU Supplemental Agreement (“MoU”)


% Complete: 100% Status: Complete

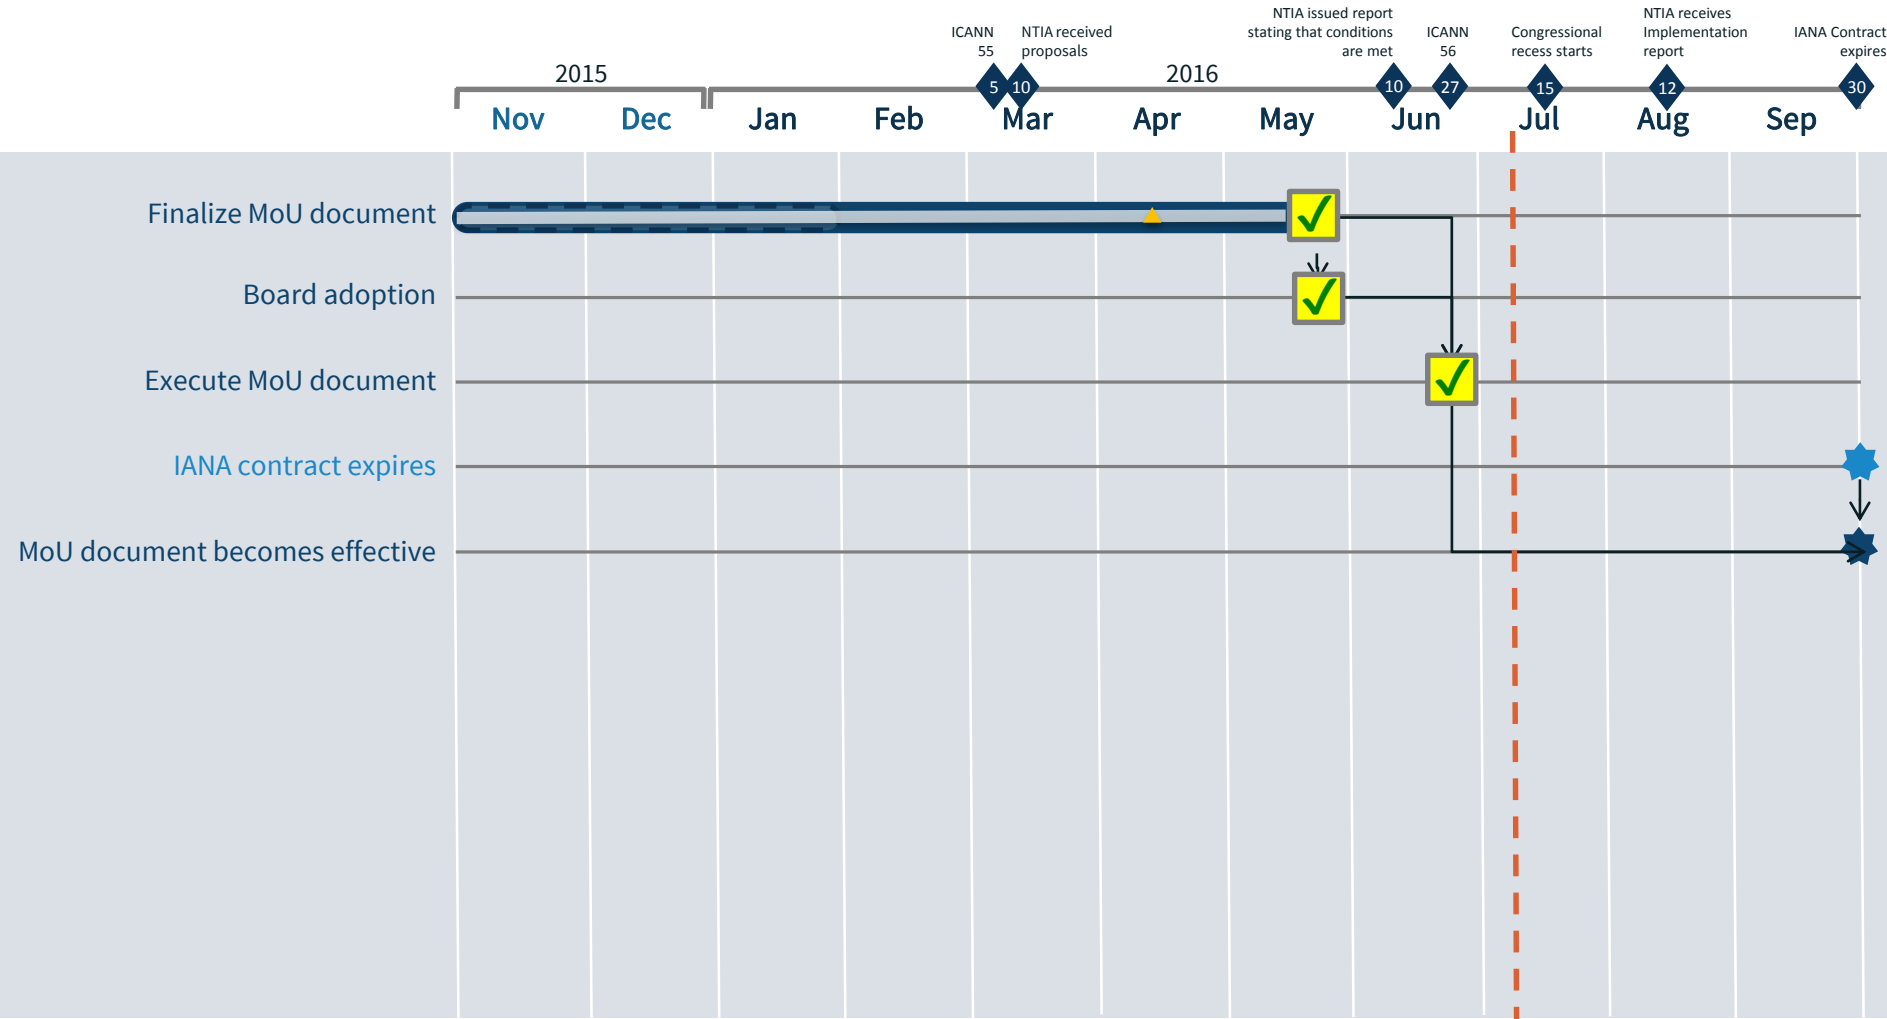

Project Updates:
 ✓ Signed the IETF MoU document.

Upcoming Activities:

Open Items:

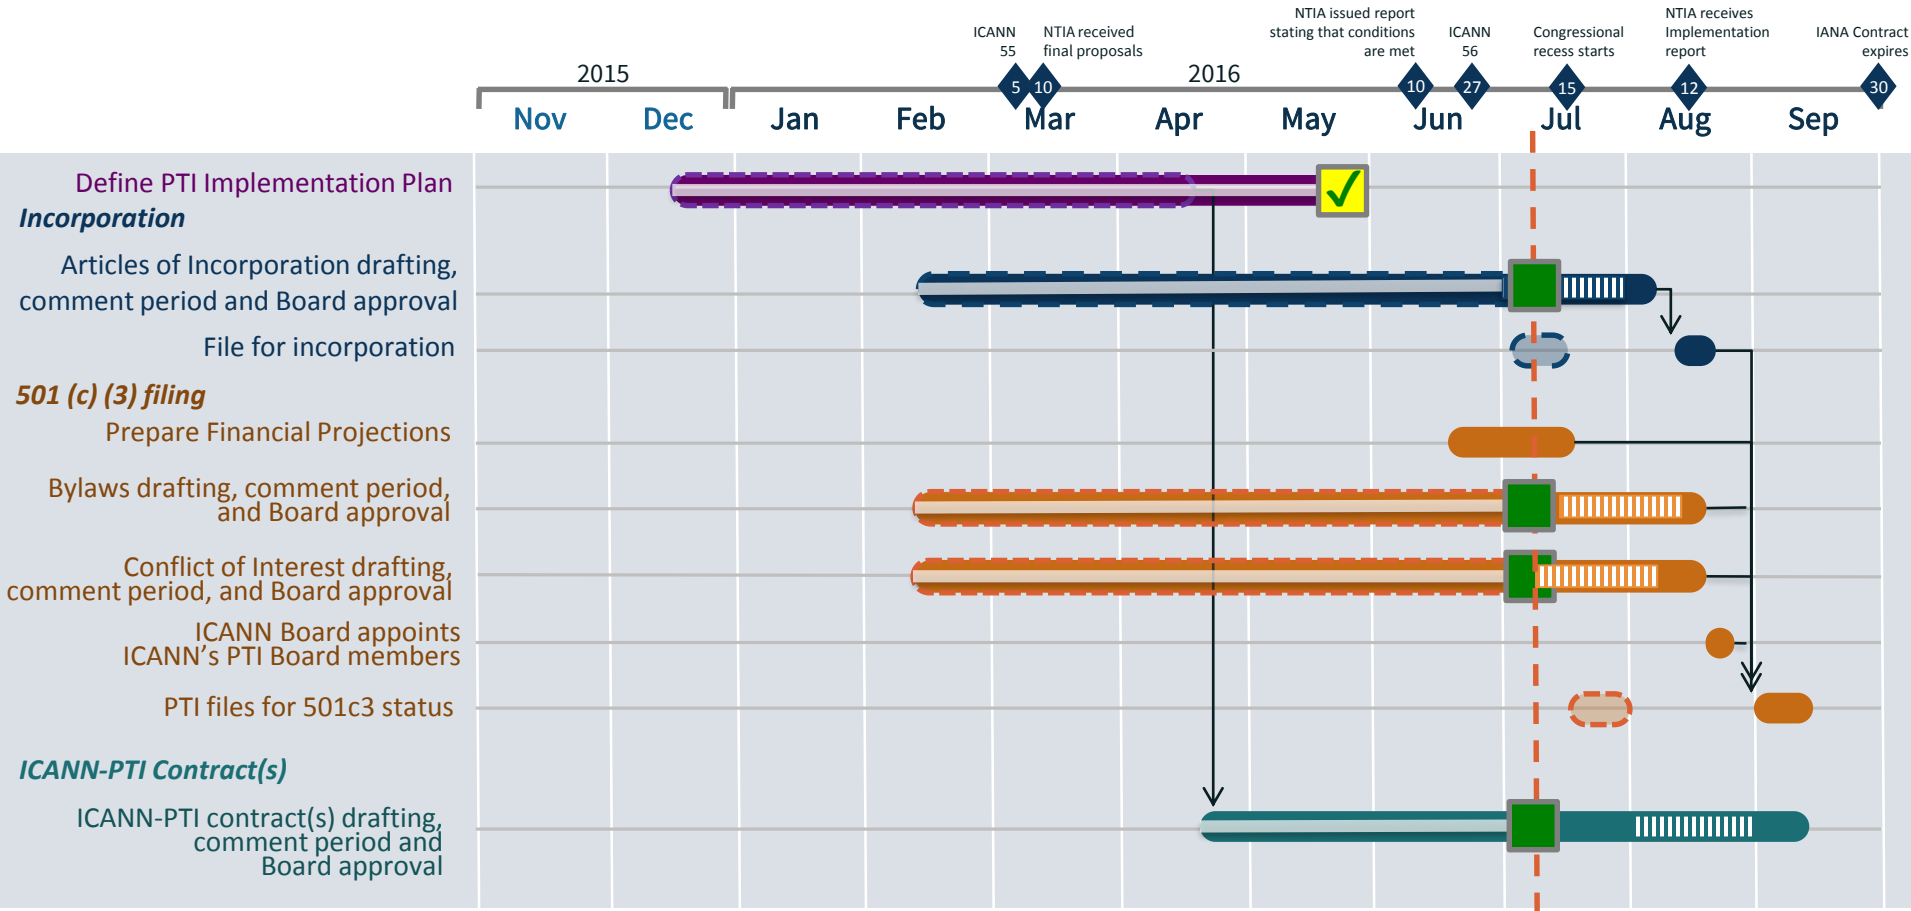

¹ Dependency on performance targets being defined by mid-July 2016 under Names SLEs project to finalize Names contract


Project Updates:

- ✓ PTI articles of incorporation, conflict of interest policy, code of conduct and expected standard of behavior posted for 30-day public comment period.

Upcoming Activities:

- Finalize PTI Bylaws for public comment posting.
- Share draft of Naming function contract with the community.

Open Items:

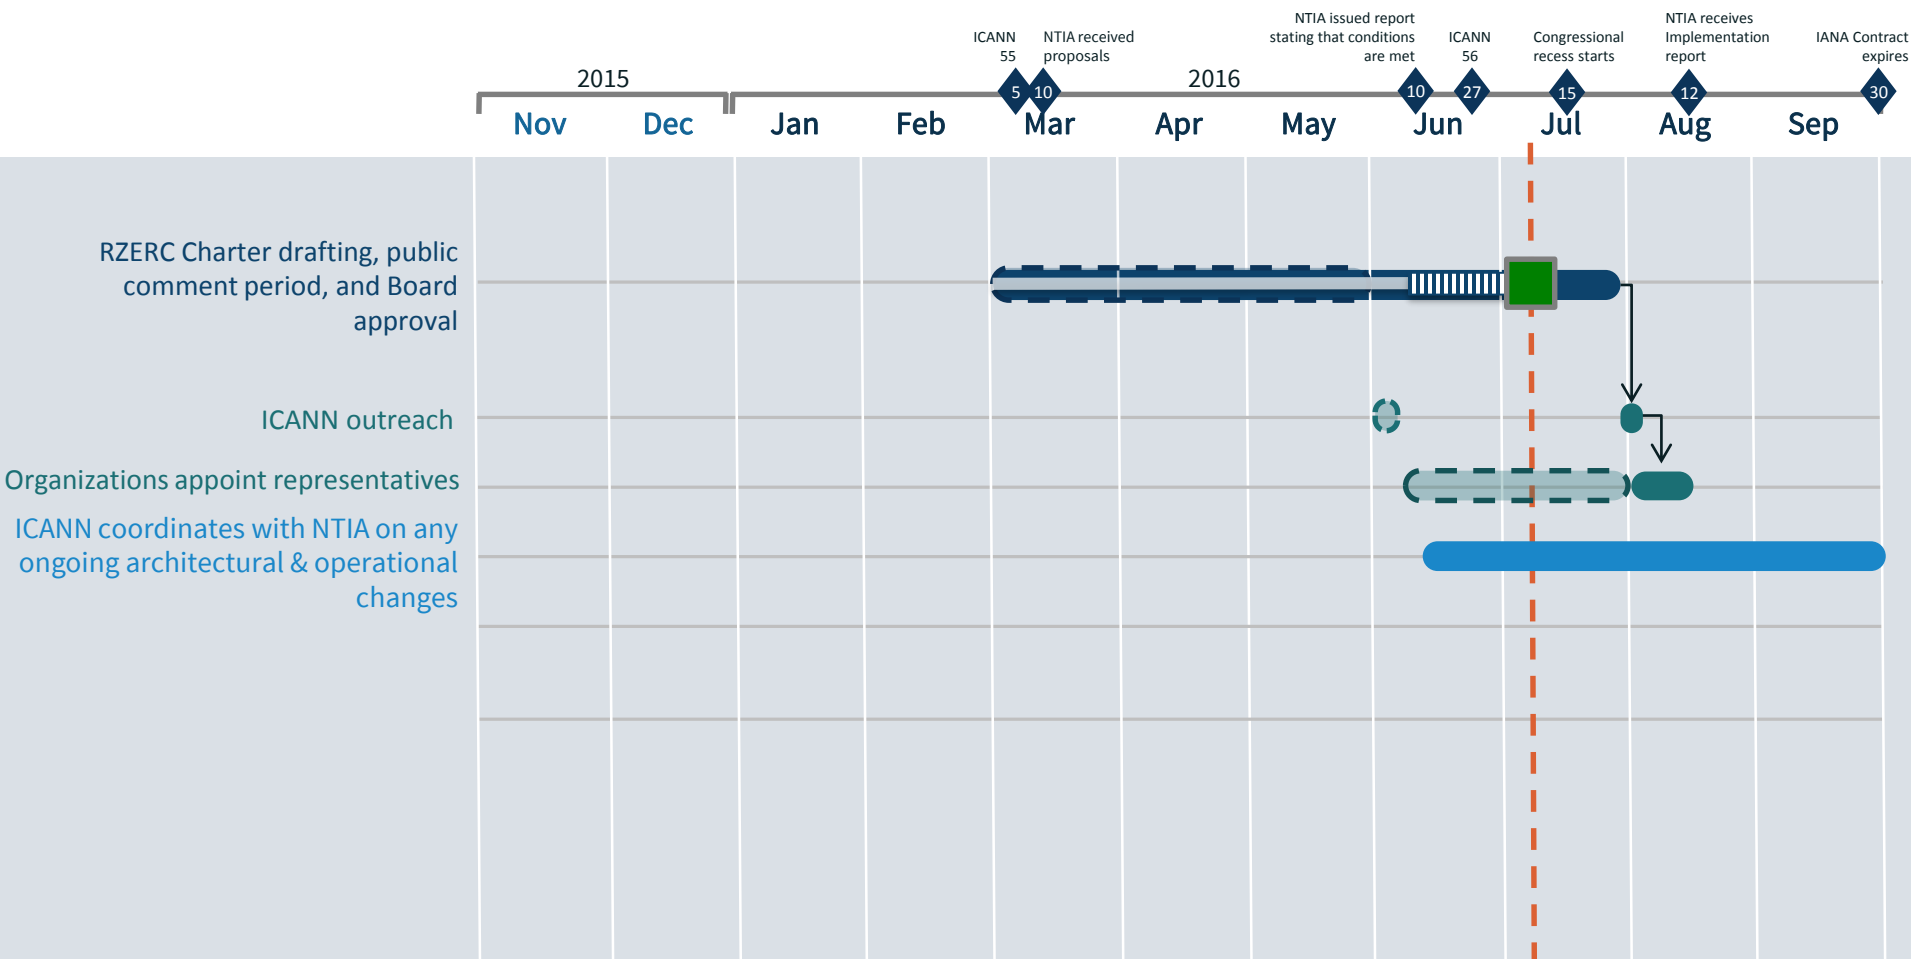


Project Updates:
 ✓ Public comment period ends on July 10.


Upcoming Activities:

- Analyze public comments on RZERC charter and revise the charter.

Open Items:



CSC Formation

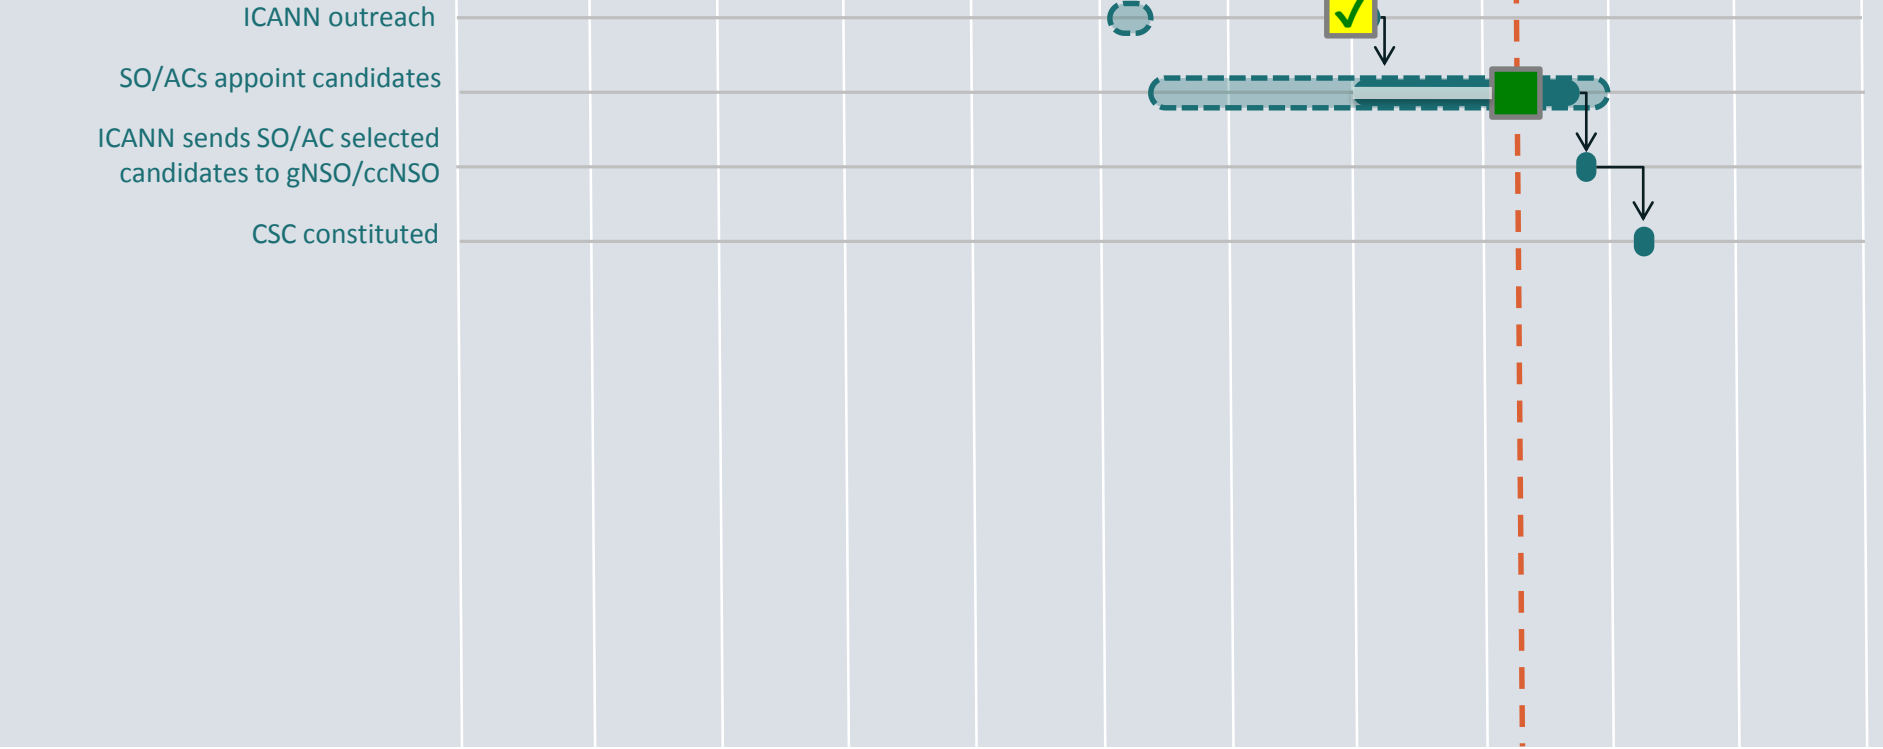


Project Updates:

- ✓ Appointing organizations working on appointing candidates.

Upcoming Activities:

- Appointing organizations submit candidates.

Open Items:

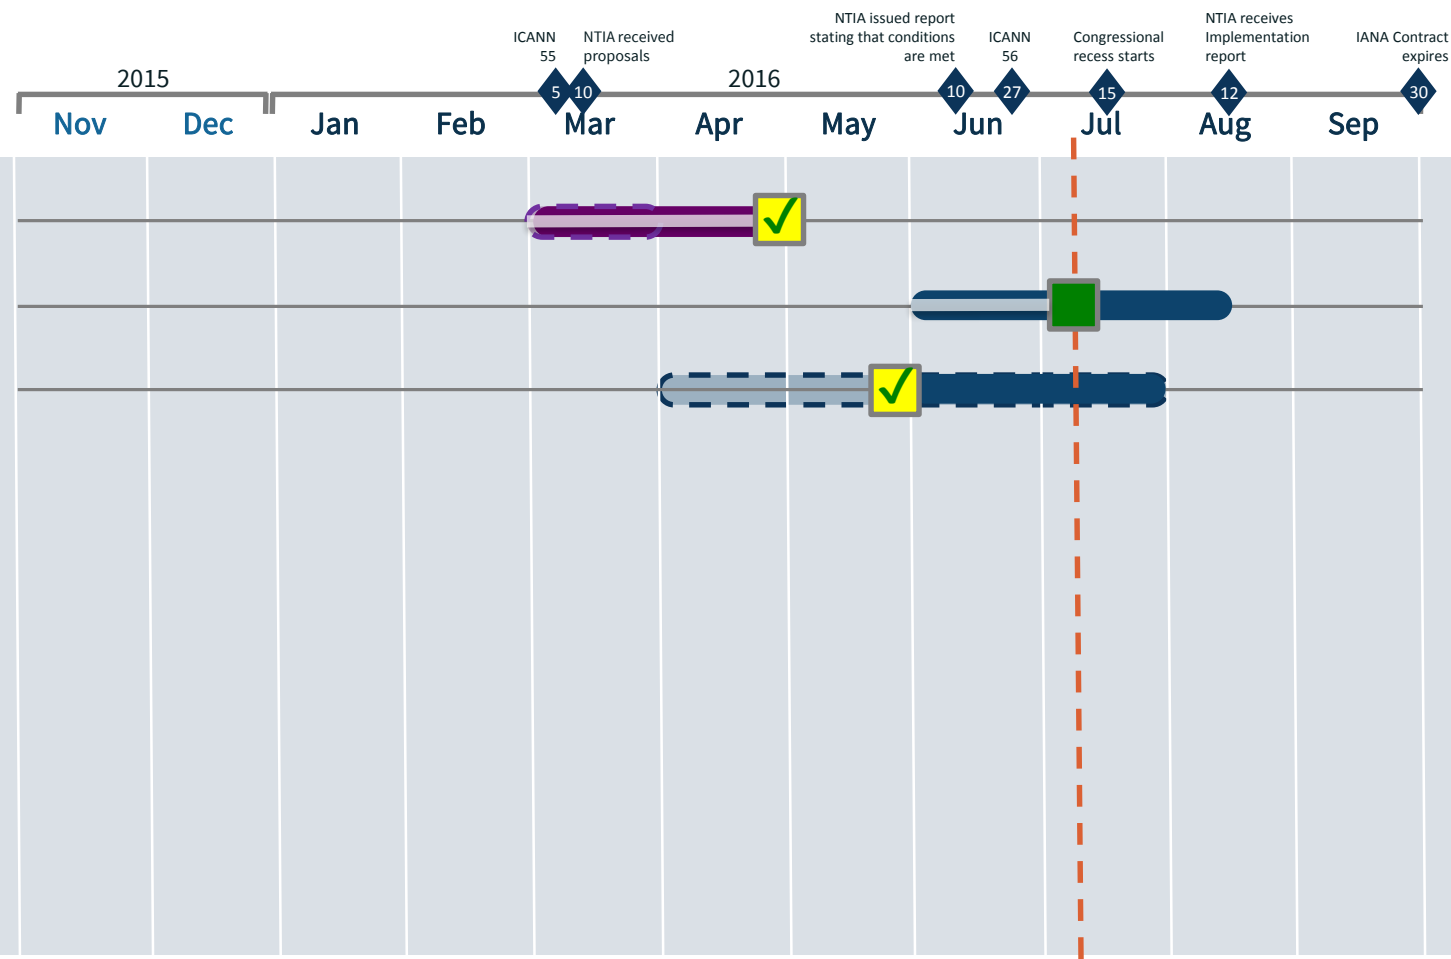


Project Updates:
 ✓ Escalation processes documentation being updated.

Upcoming Activities:

- Finalize escalation processes documentation.


Open Items:

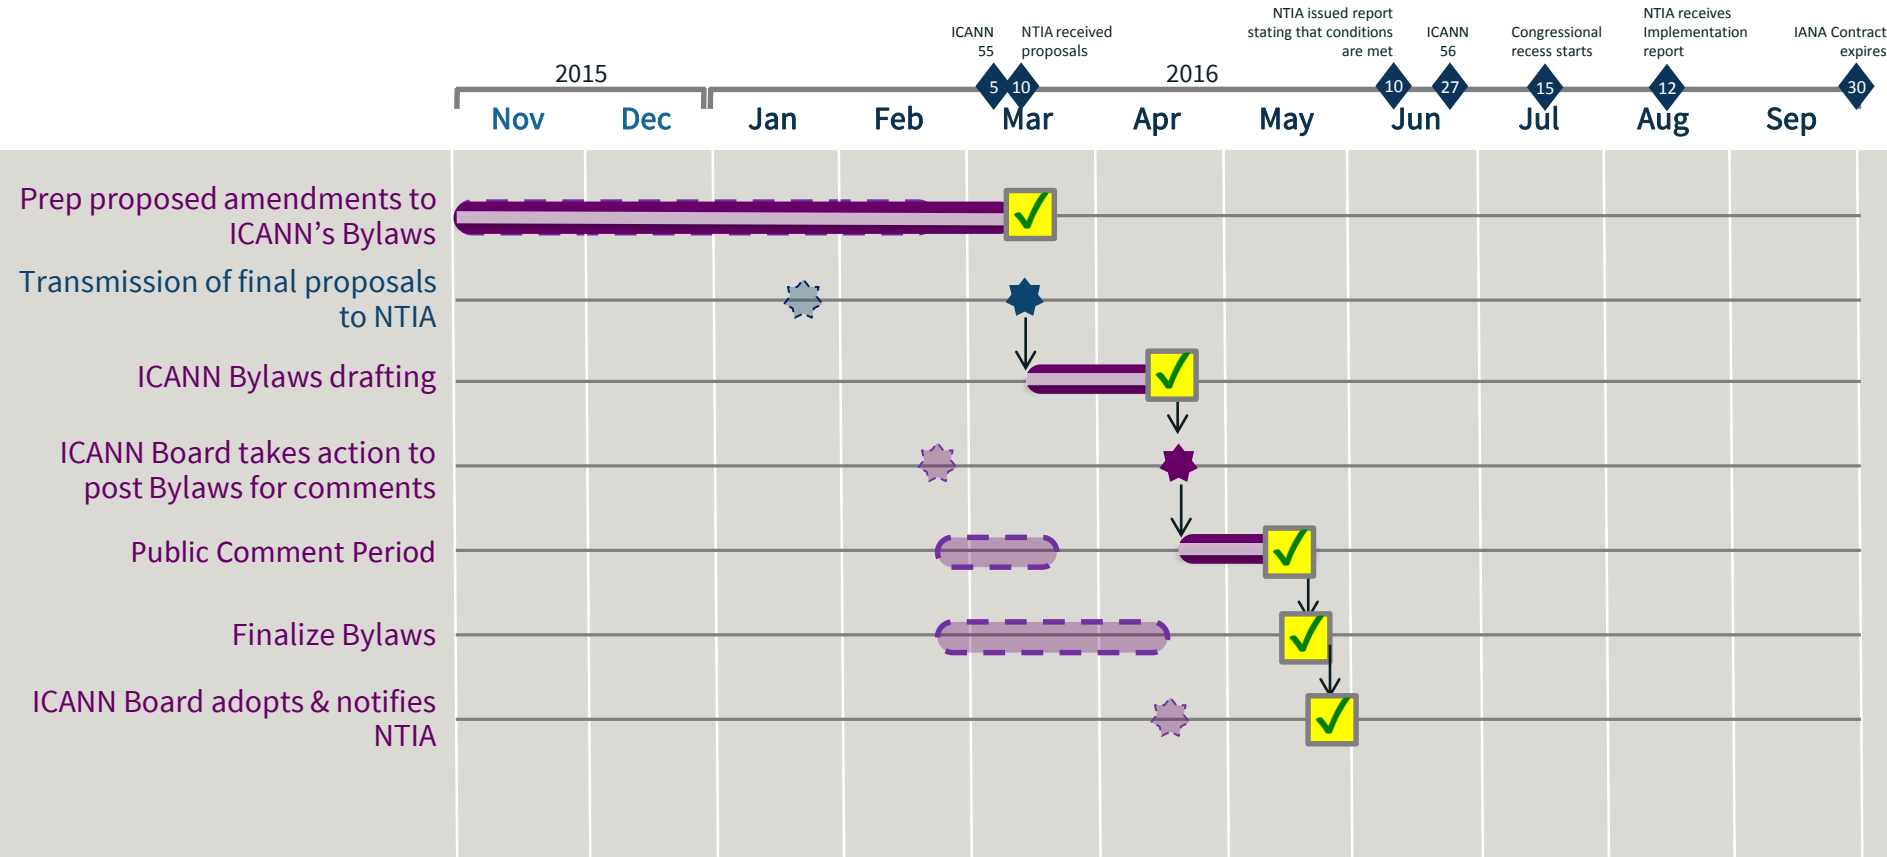

Project Updates:

Upcoming Activities:

Open Items:

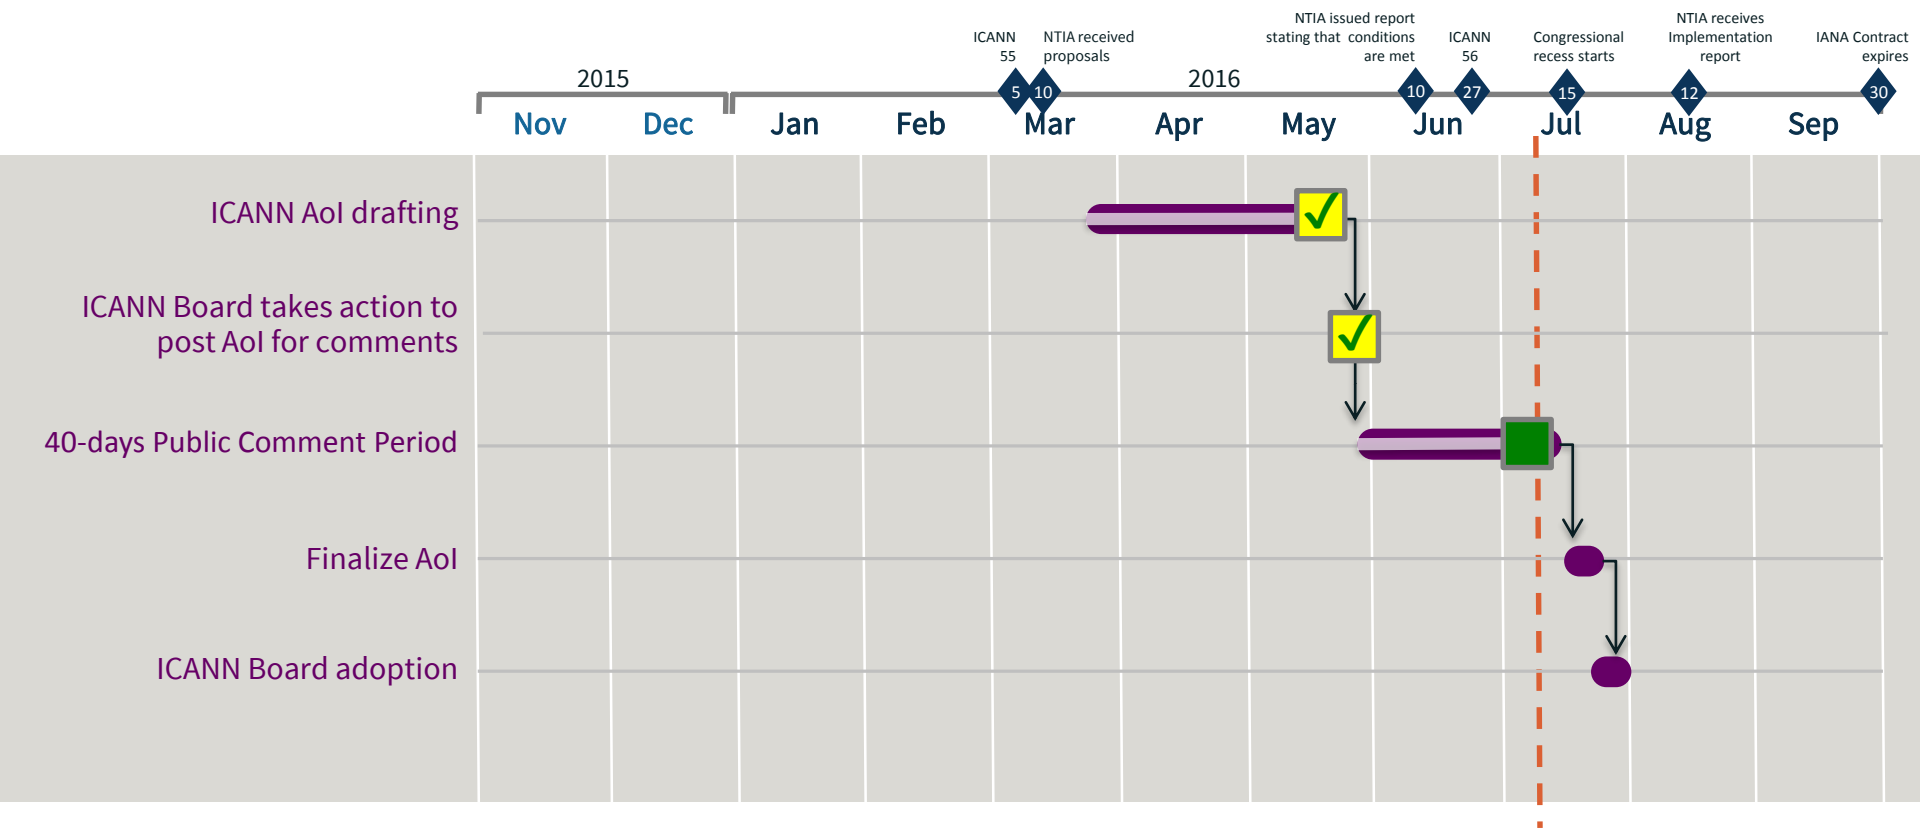

Project Updates:
 ✓ Monitoring public comments.

Upcoming Activities:


- Analyze public comments and finalize ICANN articles of incorporation.

Open Items:

Request For Reconsideration (RR) Enhancements

% Complete: 10%

Status: On-track

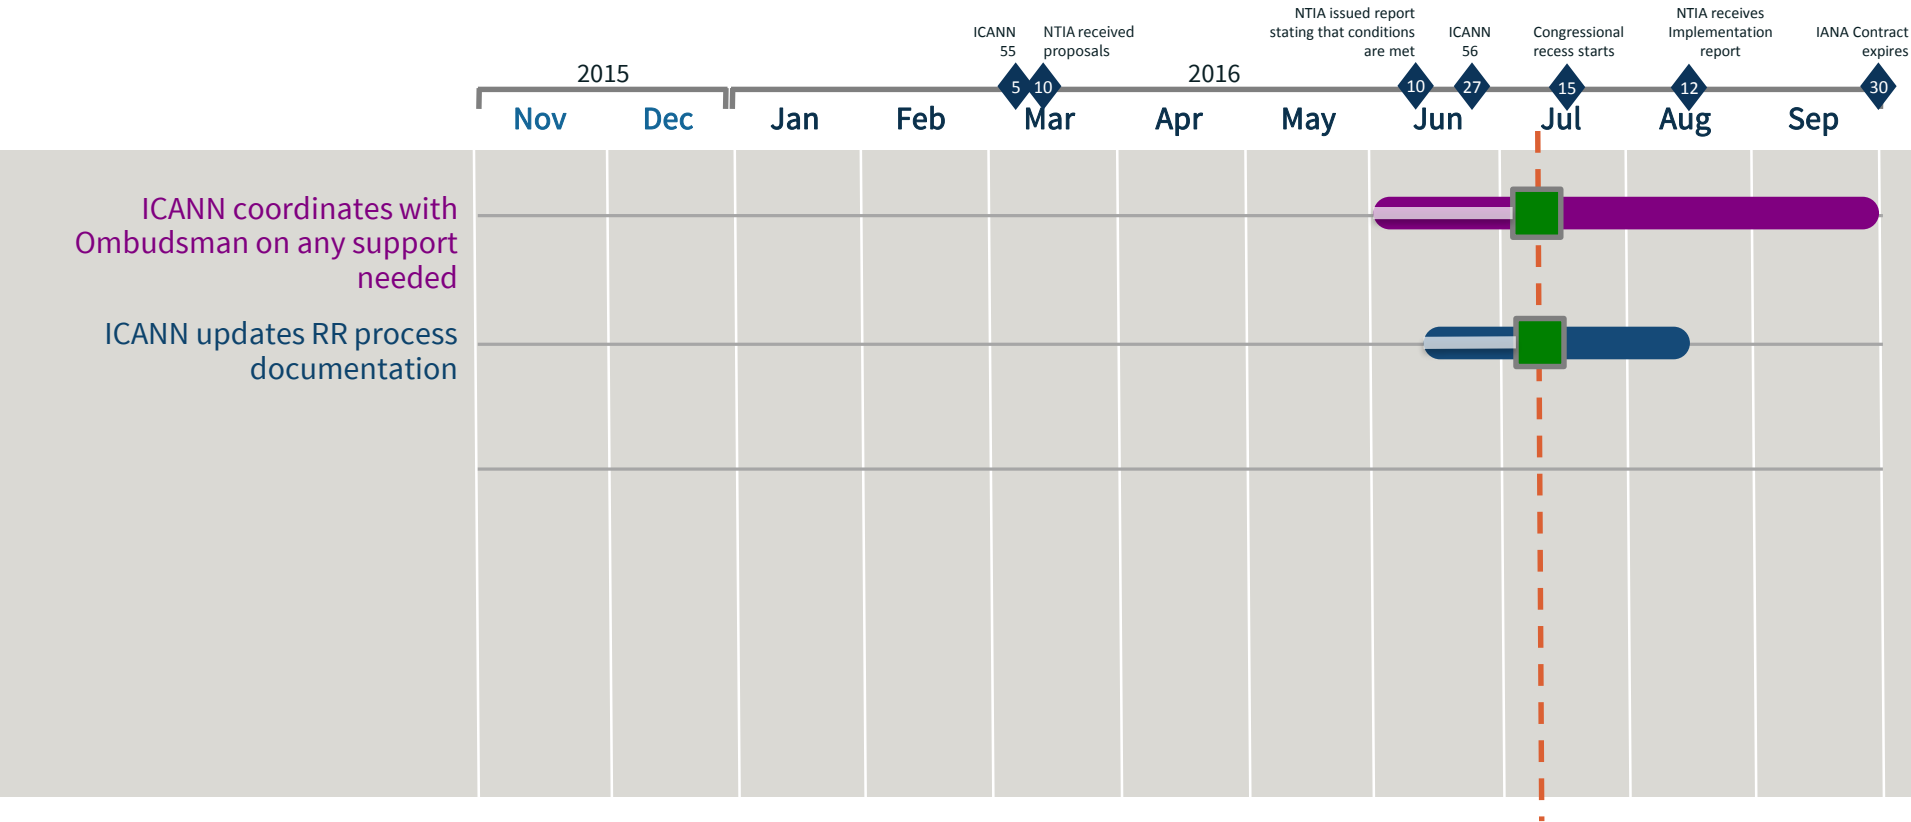

ICANN coordinates with Ombudsman on any support needed


ICANN updates RR process documentation

Project Updates:

Upcoming Activities:

- Update Request for Reconsideration process documentation.

Open Items:

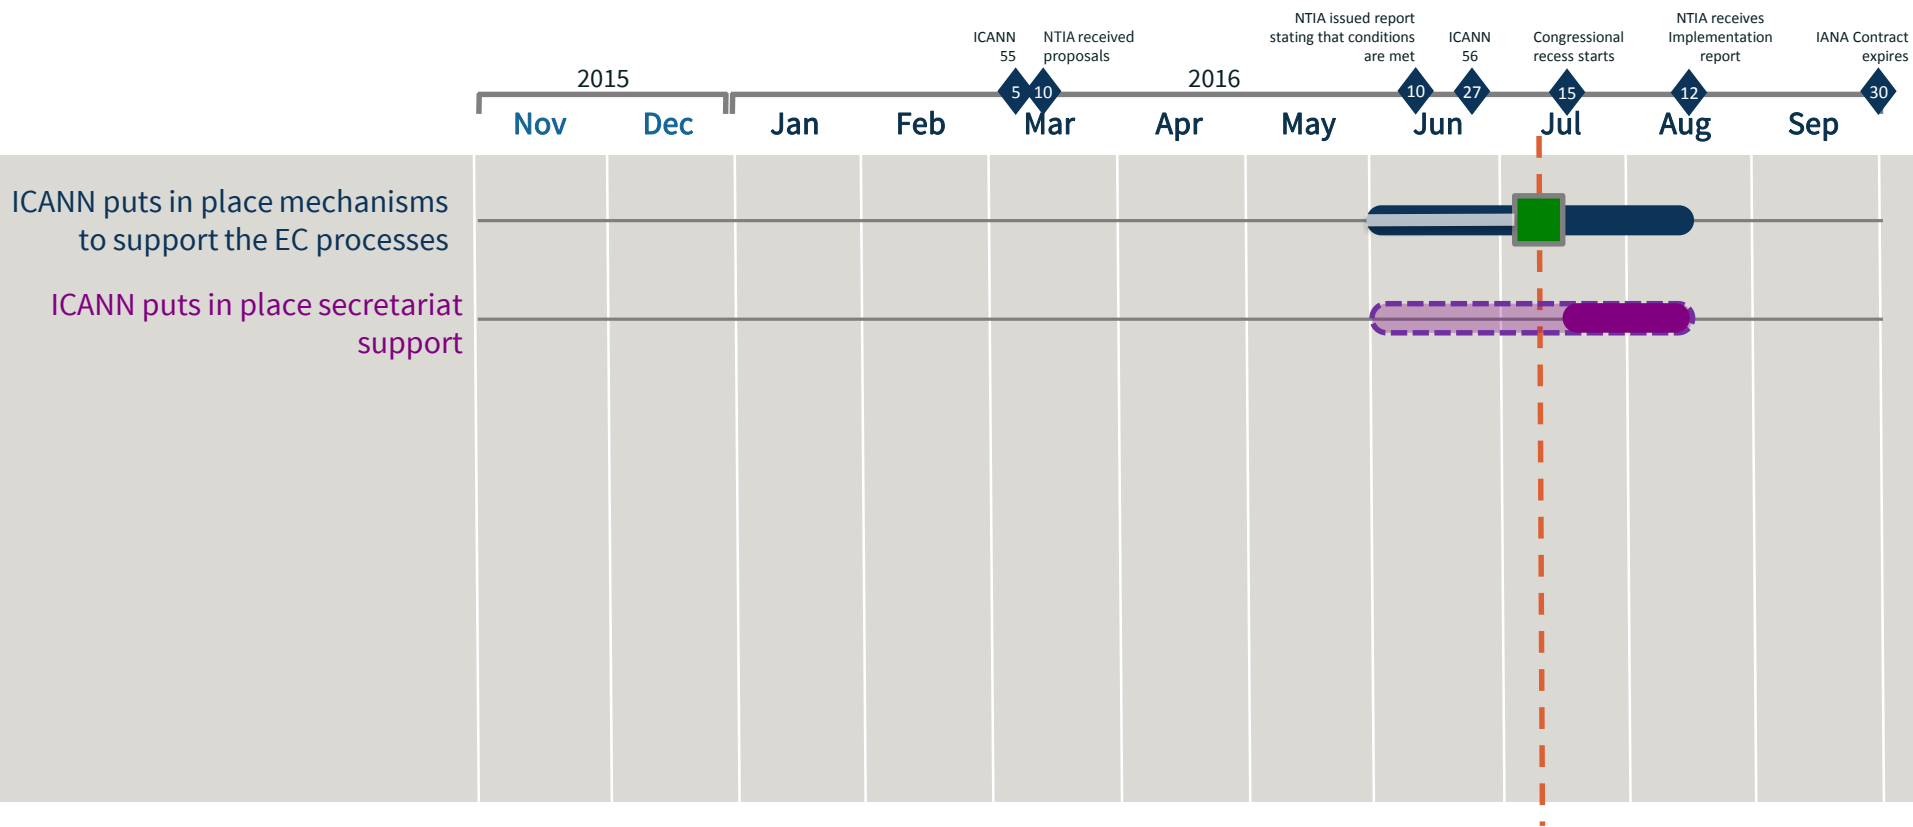


Project Updates:

- Started initial assessment of items needed to support the Empowered Community.

Upcoming Activities:

Open Items:

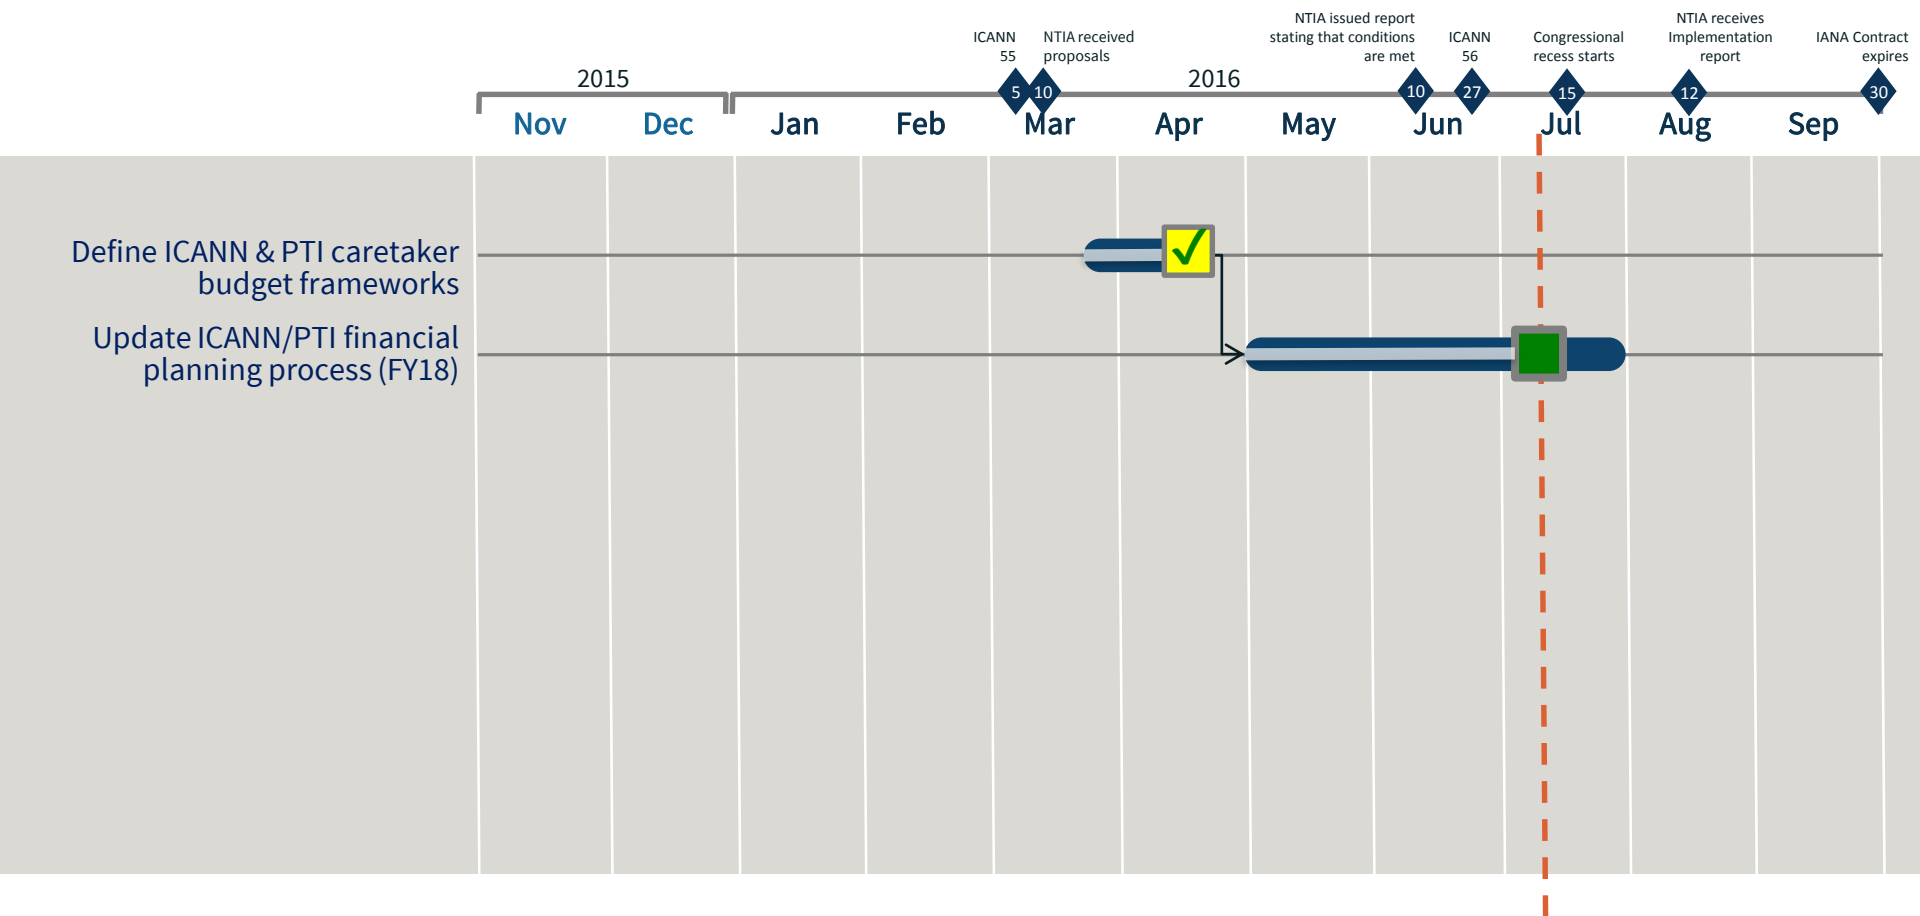

Project Updates:

Upcoming Activities:

- Finalize financial planning process.

Open Items:
